Secondary Treatment of Tijuana Sewage
P.L. 106-457, As Amended by P.L. 108-425

ID	Task Name	Estimated Duration	%	Planned Start	Planned Finish	Actual Start	Actual Finish
1	**COORDINATION WITH MEXICO**	**1371 d**	**26%**	**12/30/04**	**9/30/08**	**12/30/04**	**NA**
2	**ENVIRONMENTAL PHASE (DEVELOP SEIS)**	**275 d**	**100%**	**12/30/04**	**9/30/05**	**12/30/04**	**9/30/05**
3	Place Draft SEIS on IBWC Website	0 d	100%	12/30/04	12/30/04	12/30/04	12/30/04
4	Draft SEIS Public Review Period	61 d	100%	12/30/04	2/28/05	12/30/04	2/28/05
5	Prepare Prelim. Final SEIS	115 d	100%	3/1/05	6/23/05	3/1/05	6/23/05
6	Rvw Prelim Final SEIS	19 d	100%	6/24/05	7/12/05	6/24/05	7/12/05
7	Publish & Distribute Final SEIS	9 d	100%	7/13/05	7/21/05	7/13/05	7/21/05
8	30-day Rvw Period for Final SEIS	32 d	100%	7/29/05	8/29/05	7/29/05	8/29/05
9	Prepare Record of Decision (ROD)	68 d	100%	7/25/05	9/30/05	7/25/05	9/30/05
10	**SOLICITATION PHASE (Svc Provider)**	**363 d**	**99%**	**12/22/04**	**12/19/05**	**12/22/04**	**NA**
11	Prepare Scope & Eval Criteria	216 d	100%	12/22/04	7/25/05	12/22/04	7/25/05
12	Issue Restricted Solicitation	4 d	100%	7/26/05	7/29/05	7/26/05	7/29/05
13	Proposal Evaluation	81 d	100%	8/1/05	10/20/05	8/1/05	10/20/05
14	Negotiate & Award Contract	60 d	95%	10/21/05	12/19/05	10/21/05	NA
15	**PERMITTING PHASE**	**270 d**	**0%**	**12/20/05**	**9/15/06**	**NA**	**NA**
16	Prep. reqd US & Mx Permits Applic's	90 d	0%	12/20/05	3/19/06	NA	NA
17	Acquire Permits for Project	180 d	0%	3/20/06	9/15/06	NA	NA
18	**DESIGN PHASE**	**270 d**	**0%**	**12/20/05**	**9/15/06**	**NA**	**NA**
19	Pump Station: Prelim. Design & Analysis	120 d	0%	12/20/05	4/18/06	NA	NA
20	Pump Station: Review of Prelim Design	30 d	0%	4/19/06	5/18/06	NA	NA
21	Pump Station: Final Design	120 d	0%	5/19/06	9/15/06	NA	NA
22	Pipelines: Prelim. Design & Analysis	120 d	0%	12/20/05	4/18/06	NA	NA
23	Pipelines: Review of Prelim Design	30 d	0%	4/19/06	5/18/06	NA	NA
24	Pipelines: Final Design	120 d	0%	5/19/06	9/15/06	NA	NA
25	2ndy Fac: Prelim. Design & Analysis	120 d	0%	12/20/05	4/18/06	NA	NA
26	2ndy Fac: Review of Prelim Design	30 d	0%	4/19/06	5/18/06	NA	NA
27	2ndy Fac: Final Design	120 d	0%	5/19/06	9/15/06	NA	NA
28	**CONSTRUCTION PHASE**	**746 d**	**0%**	**9/16/06**	**9/30/08**	**NA**	**NA**
29	Pump Station	365 d	0%	9/16/06	9/15/07	NA	NA
30	Force Main & Return-flow Pipelines	550 d	0%	9/16/06	3/18/08	NA	NA
31	2ndy Wastewater Treatment Facilities	709 d	0%	9/16/06	8/24/08	NA	NA
32	Achieve Full Compliance	37 d	0%	8/25/08	9/30/08	NA	NA

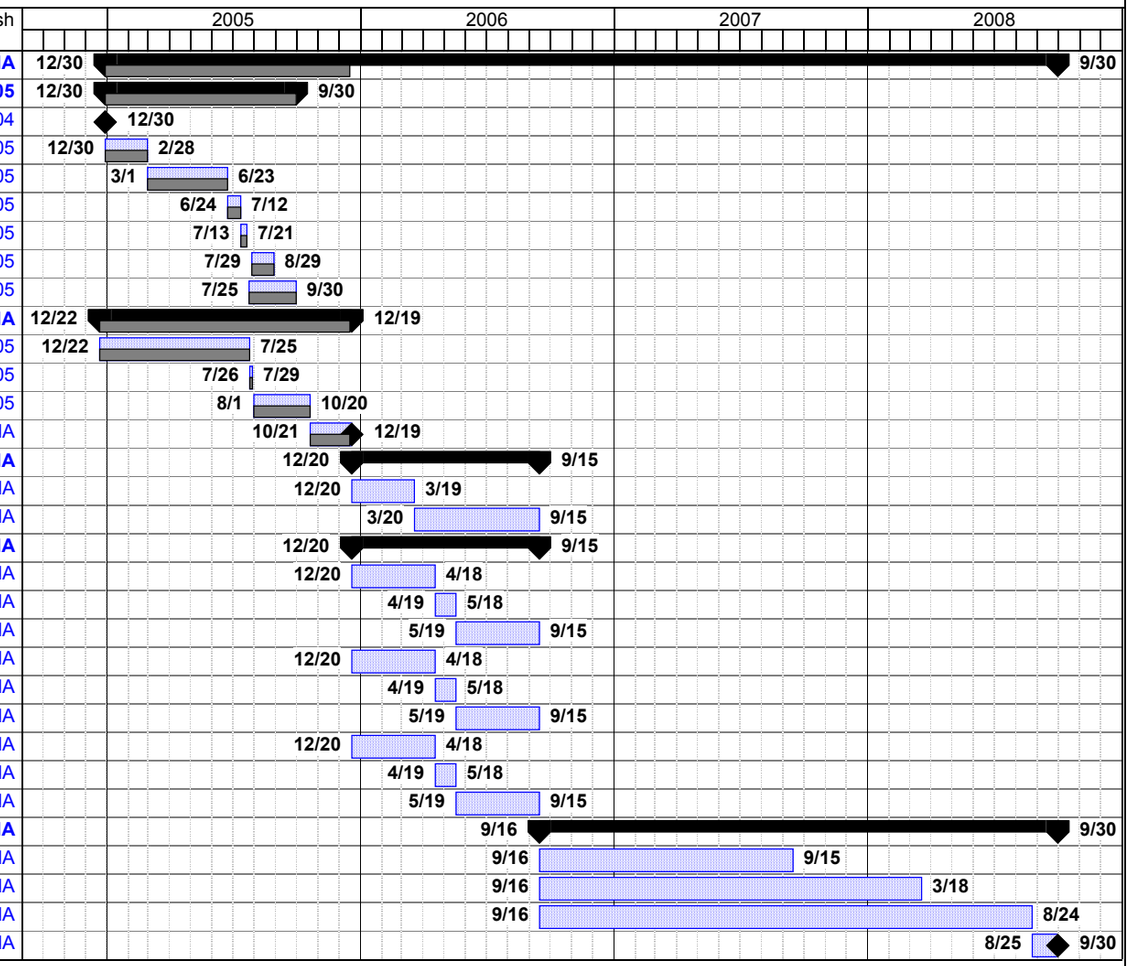

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Milestone	
Split		Summary		Rolled Up Split		External Tasks		Deadline	
Progress		Summary Progrerss		Rolled Up Milestone		Project Summary			
