FY12 & FY13 Awarded, Ongoing, & Completed Dredging Work For New Orleans District (MVN)

http://www.mvn.usace.army.mil/od/navigation.asp

Last Updated 2/1/2013

Changes made since last update
Cutterheads
Hoppers
Dustpans

All scheduled information subject to change. Does not include contingency projects.

Dredging Performed
Contract Period = Bid Date + (Award/NTP Estimated Period) + Construction Duration Allowed

Project	Solicitation No.	Contract No.	Manager	Dredge	Actuals: Dredge Start	Actuals: Dredge End	Actuals: Actual Bid Date
MISS RIV SWP LSD CUTTER/DUSTPAN #1-2010	10B0055	11C0024	Spraul	"Dredge 32"	2/25/2011	7/15/2011	1/20/2011
ATCH BASIN, GIWW & MISC. CDR #2-10	10B0049	11C0053	Lowe	"Missouri H."	7/27/2011	9/30/2011	7/20/2011
MISS RIV NEW ORLEANS HARBOR CUTT 1-2011	11B0021	11C0052	Spraul	"GD Morgan"	7/25/2011	9/13/2011	7/18/2011
ATCHAF RIV BAY, BAR, HSHOE & MISC PROJ CDR 1-2011	11B0030	11C0054	Lowe	"Dredge 32"	8/8/2011	10/26/2011	7/28/2011
OUTLETS OF VENICE BAPTISTE COLLETTE BAR CHANNEL	09B0074	11C0063	Schneider	"Missouri H."	10/9/2011	12/12/2011	8/31/2011
ATCH BAR CH. MD CY 475+00 TO 1355+00	10B0069	11C0071	Lowe	"GD Morgan"	9/27/2011	11/18/2011	9/13/2011
EAST & WEST CALUMET FLOODGATES MD CY	11B0048	11C0067	Falk	Bucket Dredge "Chief"	11/5/2011	11/28/2011	9/14/2011
MISS RIV SWP LSD CUTTER/DUSTPAN #1-2011	11B0034	11C0014	Spraul	"Marion"	3/10/2012	4/19/2012	2/7/2012
MISS RIV NOH & BAYOU LAFOURCHE CDR #2-2011	11B0022	12C0020	Spraul/Schneider	"Missouri H."	3/15/2012	6/9/2012	3/6/2012
MISS RIV SWP LSD CUTTER/DUSTPAN #2-2011	11B0035	12C0021	Spraul	"California"	4/20/2012	7/9/2012	3/20/2012
OUTLETS OF VENICE TIGER PASS MD (MI 7.3 TO 14.0) 1-11	11B0046	12C0024	Schneider	"Missouri H."	6/22/2012	11/5/2012	4/12/2012
CALCASIEU RIVER MI 5 TO 17 MD	12B0026	12C0030	Falk	"Leonard J"	6/29/2012	11/13/2012	5/1/2012
ATCHAF RIV BAR CH, CHENE, BOEUF, & BLACK MD 2-2010	10B0070	12C0033	Lowe	"Alaska"	7/23/2012	11/7/2012	5/15/2012
ATCHAF RIV BERWICK BAY THREE RIVERS CDR IDIQ	12B0027	12D0007	Lowe	"Borinquen"	7/24/2012	1/9/2013	6/7/2012
MISS RIV SWP HDDA CY MD	12B0028	12C0034	Spraul	"MaCaskill"	9/10/2012		6/11/2012
OUTLETS OF VENICE, BAP COLL BAR CH, MD 1-2011	11B0037	12C0041	Schneider	"E Stroud"	9/7/2012	12/20/2012	7/17/2012
ATCHAF RIV BAY CHANN CY MD 1-2010	10B0078	12C0042	Lowe	"Captain Frank"	11/26/2012	1/12/2013	7/18/2012
MISS RIV SALTWATER BARRIER SILL CDR 1-2012	12B0043	12C0044	Spraul	"Texas", "California"	8/16/2012	9/18/2012	8/9/2012
CALCASIEU RIVER MI 34 TO 36 MD	12B0046	12C0056	Falk				9/25/2012
MISS RIV HOH (HOUMA & GIWW) CDR 3-2011	11B0023	12C0051	Schneider	"Borinquen"	10/17/2012	11/11/2012	9/13/2012
MISS RIV ORCS LOW SILL & AUX CS INFLOW CHAN DRDG	12B0033	12C0039	Beauvais	"GD Morgan"	9/11/2012	1/22/2013	7/3/2012
CALCASIEU RIVER MI 17 TO 34 MD			Falk				

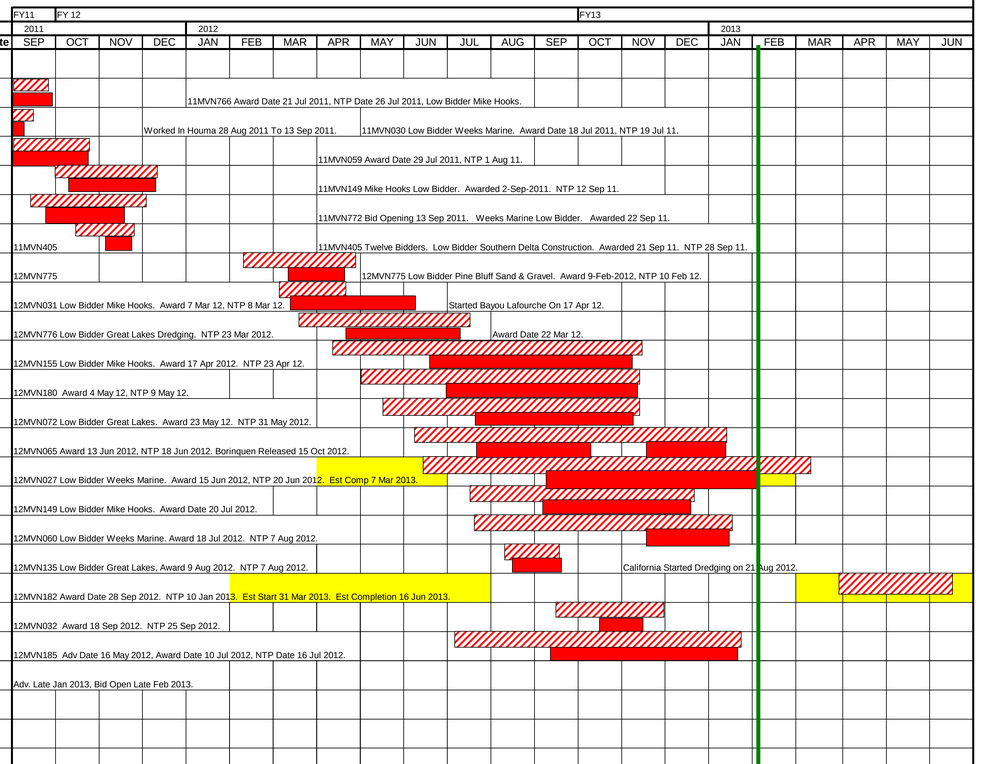

FY12 & FY13 Awarded, Ongoing, & Completed Dredging Work For New Orleans District (MVN)

http://www.mvn.usace.army.mil/od/navigation.asp

Last Updated 2/1/2013

Changes made since last update
Cutterheads
Hoppers
Dustpans

All scheduled information subject to change. Does not include contingency projects.

Dredging Performed
Contract Period = Bid Date + (Award/NTP Estimated Period) + Construction Duration Allowed
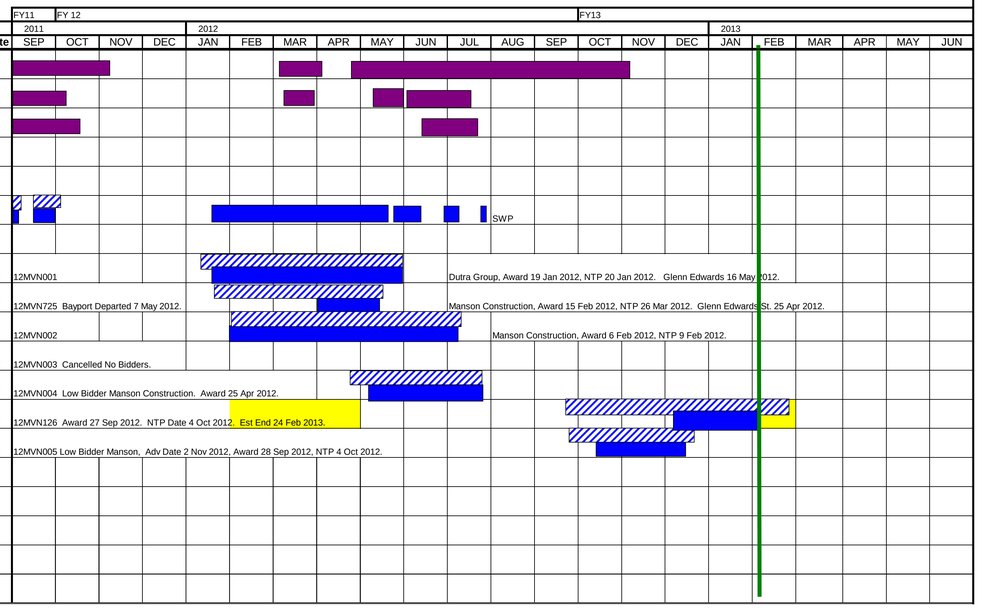
Project	Solicitation No.	Contract No.	Manager	Dredge	Actuals: Dredge Start	Actuals: Dredge End	Actuals: Actual Bid Date
MISSISSIPPI RIVER DEEP DRAFT CROSSINGS		DACW66-01C0016	Spraul	"Wallace McGeorge"	4/20/2012	11/6/2012	
MISSISSIPPI RIVER DEEP DRAFT CROSSINGS	**Gov't**		Spraul	"Jadwin"	6/3/2012	7/16/2012	
MISSISSIPPI RIVER SHALLOW DRAFT CROSSINGS	**Gov't**		Spraul	"Hurley"	6/12/2012	7/21/2012	
MISS RIV SWP GOV'T HOPPER	**Gov't**		Gov't	"McFarland"	8/7/2010	8/26/2010	
MISS RIV SWP GOV'T HOPPER EXERCISE	**Gov't**		Gov't	"Wheeler" A-SWP, B-Xings, C-NOH	7/27/2012	7/28/2012	
MISS RIV SWP LSD HOPPER #1-2012	**12B0006**	**12C0008**	Spraul	"Stuyvesant", "Glenn Edward	1/21/2012	5/31/2012	1/10/2012
CALCASIEU RIVER BAR CHANNEL HOPPER #1-2011	**11B0024**	**12C0017**	Falk	"Bayport", "Glenn Edwards"	4/2/2012	5/14/2012	1/24/2012
MISS RIV SWP LSD HOPPER #2-2012	**12B0007**	**12C0013**	Spraul	"Newport"	2/13/2012	7/8/2012	2/1/2012
MISS RIV SWP LSD HOPPER #3-2012 (CANCELLED NO BIDDERS)	**12B0008**	**N/A**	Spraul	N/A	N/A	N/A	2/16/2012
MISS RIV SWP LSD HOPPER #4-2012	**12B0009**	**12C0029**	Spraul	"Bayport"	5/8/2012	7/27/2012	4/24/2012
CALCASIEU RIVER BAR CHANNEL HOPPER #2-2011	**11B0025**	**12C0058**	Falk	"Newport"	12/6/2012		9/25/2012
MISS RIV SWP LSD HOPPER #5-2012 (GALVESTON)	**12B0010**	**12C0023**	Maria Rodriguez, Galveston	"Bayport"	10/12/2012	12/10/2012	9/26/2012
****CWPPRA project has an MVN maintenance dredging component**							
CWPPRA projects last updated 19 Aug 2010, S. Hennington
