

A0006985

AMENDMENT OF SOLICITATION/MODIFICATION OF CONTRACT				1. CONTRACT ID CODE 077	PAGE OF PAGES 1 2
2. AMENDMENT/MODIFICATION NO. P00006		3. EFFECTIVE DATE 03/07/95	4. REQUISITION/PURCHASE REQ. NO.		5. PROJECT NO. (If applicable) CIN-02
6. ISSUED BY US ARMY ENGR DIST NEW ORLEANS PO BOX 60267 NEW ORLEANS LA 70160-0267 Cynthia Whitten		CODE ISSUE1	7. ADMINISTERED BY (If other than Item 6) CELMN-CT-CC MS. WHITTEN PHONE: (504) 862-1899		CODE modcw
8. NAME AND ADDRESS OF CONTRACTOR (No., street, county, State and ZIP Code) Vendor ID: 00001344 B&K CONSTRUCTION 1905 HIGHWAY 59 MANDEVILLE LA 70448			(X)	9A. AMENDMENT OF SOLICITATION NO.	
				9B. DATED (SEE ITEM 11)	
			X	10A. MODIFICATION OF CONTRACT/ORDER NO. DACW29-94-C-0079	
				10B. DATED (SEE ITEM 13) 07/11/94	
CODE OGTN3	FACILITY CODE				

11. THIS ITEM ONLY APPLIES TO AMENDMENTS OF SOLICITATIONS

The above numbered solicitation is amended as set forth in Item 14. The hour and date specified for receipt of Offers is extended, is not extended. Offers must acknowledge receipt of this amendment prior to the hour and date specified in the solicitation or as amended, by one of the following methods: (a) By completing Items 8 and 15, and returning _____ copies of the amendment; (b) By acknowledging receipt of this amendment on each copy of the offer submitted; or (c) By separate letter or telegram which includes a reference to the solicitation and amendment numbers. FAILURE OF YOUR ACKNOWLEDGMENT TO BE RECEIVED AT THE PLACE DESIGNATED FOR THE RECEIPT OF OFFERS PRIOR TO THE HOUR AND DATE SPECIFIED MAY RESULT IN REJECTION OF YOUR OFFER. If by virtue of this amendment you desire to change an offer already submitted, such change may be made by telegram or letter, provided each telegram or letter makes reference to the solicitation and this amendment, and is received prior to the opening hour and date specified.

12. ACCOUNTING AND APPROPRIATION DATA (If required) Mod Obligated Amount US \$9,263.77
Funds in the amount of \$9,263.77 are available. See Attached.



13. THIS ITEM APPLIES ONLY TO MODIFICATIONS OF CONTRACTS/ORDERS, IT MODIFIES THE CONTRACT/ORDER NO. AS DESCRIBED IN ITEM 14.

(X)	A. THIS CHANGE ORDER IS ISSUED PURSUANT TO: (Specify authority) THE CHANGES SET FORTH IN ITEM 14 ARE MADE IN THE CONTRACT ORDER NO. IN ITEM 10A.
X	CC I.83 Changes
	B. THE ABOVE NUMBERED CONTRACT/ORDER IS MODIFIED TO REFLECT THE ADMINISTRATIVE CHANGES (such as changes in paying office, appropriation date, etc.) SET FORTH IN ITEM 14, PURSUANT TO THE AUTHORITY OF FAR 43.103 (b).
	C. THIS SUPPLEMENTAL AGREEMENT IS ENTERED INTO PURSUANT TO AUTHORITY OF:
	D. OTHER (Specify type of modification and authority)

E. IMPORTANT: Contractor is not, is required to sign this document and return original copies to the issuing office.

14. DESCRIPTION OF AMENDMENT/MODIFICATION (Organized by UCF section headings, including solicitation/contract subject matter where feasible.)
The following change is made to the above numbered contract for Lake Pontchartrain, LA & Vicinity, HLP, London Avenue Outfall Canal, Parallel Protection, Mirabeau Avenue to Leon C. Simon Boulevard Floodwall, Orleans Parish, LA, to provide a wooden fence at the staging area.

Except as provided herein, all terms and conditions of the document referenced in Item 9A or 10A, as heretofore changed, remains unchanged and in full force and effect.

15A. NAME AND TITLE OF SIGNER (Type or print) H. B. Kenyon, President		16A. NAME AND TITLE OF CONTRACTING OFFICER (Type or print) Chester Ashley, ACO 007	
15B. CONTRACTOR/OFFEROR  Signature of person authorized to sign		15C. DATE SIGNED 3/9/95	16B. UNITED STATES OF AMERICA BY  (Signature of Contracting Officer)
			16C. DATE SIGNED 3-10-95

ORIGINAL

1st det made

dt 3/14/55

2nd det

dt 4/10/55

SF 30 CONTINUATION SHEET

12. Accounting and Appropriation Data (Cont.)

96X8862 FWL2111000NOLML

14. Description of Amendment/Modification (Cont.)

CHANGES TO THE BIDDING SCHEDULE: The schedule of Contract Items, Descriptions, Estimated Quantities, Units, Unit Prices, and Estimated Amounts is modified as follows:

Item No.	Description	Estimated Quantity	Unit	Unit Price	Estimated Amount	Amount of Change
0022	Fencing (CIN-02)	LUMP SUM	LS	-----	\$9,263.77	(+) \$9,263.77

CHANGES TO THE CONTRACT SPECIFICATIONS: Add the following sentence to the end of paragraph C2F-1: "The work also consists of providing and installing a wooden fence fronting the field office, to obstruct the view of the staging area by the residents located directly across the street."

Add new paragraph C2F-5.1 as follows: "C2F-5.1. MEASUREMENT AND PAYMENT. (CIN-02). Work for providing and installing a wooden fence at the field office will not be measured for payment. Payment for the wooden fence will be made at the lump sum price for "Fencing (CIN-02)." Price and payment shall include all costs for providing and installing the wooden fence and for all costs associated with the return and restocking of the privacy slats."

CHANGES TO THE CONTRACT DRAWINGS: There are no changes to the contract drawings.

CHANGES TO THE CONTRACT PRICE: The contract price is increased by \$9,263.77.

CHANGES TO THE CONTRACT TIME: The contract time remains unchanged.

It is further understood and agreed that this adjustment constitutes compensation in full on behalf of the contractor, its subcontractors and suppliers for all costs and markups directly or indirectly attributable to the changes ordered for all delays, impacts, and extended overhead related thereto, and for performance of the change within the time frame stated.

PRICE NEGOTIATION MEMORANDUM

Lake Ponchartrain, Louisiana and Vicinity,
High Level Plan,
London Avenue Outfall Canal,
Parallel Protection,
Mirabeau Avenue to Leon C. Simon Boulevard Floodwall,
Orleans Parish, Louisiana
Contract Number DACW29-94-C-0079, CIN 02
B & K Construction Co., Inc.

1. CONTRACT DESCRIPTION. The subject contract was awarded on 11 July 1994 in the amount of \$4,554,500.00. The contract consists of clearing and grubbing, selective demolition, demolition of a pedestrian bridge, structural excavation and backfill, fertilizing seeding, and mulching, cutting existing sheet piling, pulling existing sheet piling, redriving existing sheet piling, providing and installing new sheet piling, painting, constructing reinforced concrete floodwalls, constructing concrete slope pavement, utility modifications, relocation of feeder lines, erosion control, and temporary flood protection and cofferdams.

2. DESCRIPTION OF MODIFICATION.

a. SUMMARY AND NECESSITY FOR CHANGE. The user, the Orleans Levee District, requested slats be added to the fencing to obstruct the view of the staging area by the residents directly across the street. When installation of the slats began, the contractor was ordered to cease operations because the slats did not provide adequate coverage. It was decided to use a wooden fence as an alternative.

b. REASON FOR OMISSION FROM PLANS AND SPECIFICATIONS. It was realized subsequent to award at the request of the Orleans Levee District.

c. AUTHORITY FOR MODIFICATION: This change is issued under the authority provided by Contract Clause I.83 Changes.

3. PRICE AND TIME JUSTIFICATION:

a. SUMMARY.

<u>Contractor Proposal</u>	<u>Government Estimate</u>	<u>Revised G.E.</u>	<u>Negotiated Settlement</u>
\$9,311.94	\$9,253.84	\$9,299.65	\$9,263.77

b. PRICING STRATEGY. A price analysis was used to evaluate the contractor's proposal using independent Government Estimates which were prepared based on site specific resources and standard industry practices.


c. Participants. Mr. Kennon was the Lead Negotiator for B & K Construction Co., Inc., and Mr. Stradford Goins was the Lead Negotiator for the Government.

d. NEGOTIATION SUMMARY. By verbal request on 5 January 1995 the Government requested a proposal from the contractor to delete adding slats to the fencing around the field office and replace the fence with a wooden fence to obstruct the view of the staging area by the residents directly across the street. An independent Government estimate was prepared on 16 January 1995 in the amount of \$9,253.84. The contractor proposal was received on 11 January 1995 in the amount of \$9,311.94. On 16 February 1995, via telephone, the contractor was informed that his proposal in the amount of \$9,311.94 did not compare favorably to the government estimate. The contractor was informed that the labor charged should have been included in overhead. Also, the profit exceeded the profit computed using the weighted guidelines method. The contractor also noted that his proposal did not include bond. The Government agreed to allow the bond expense and the contractor agreed to revise his proposal accordingly to reflect all the changes we discussed. The Government Estimate was revised from \$9,253.84 to \$9,299.65 to reflect the actual bond rate of 1.5% in lieu of the estimated 1% bond rate. The contractor's revised proposal of \$9,263.77 was considered to be fair and reasonable and was accepted. The contractor also agreed that this modification eliminated all impacts to the contract as a result of this change and that the contract time be remained unchanged.

4. APPROPRIATION DATA. Funds in the amount of \$9,263.77 are available under Appropriation 96X8862, Contributed Funds, Account No. FWL21 1100 ON OLML, Accounting Element 284.

SUBMITTED FOR APPROVAL

Date: 17 February 1995


STRADFORD GOINS
Lead Government Negotiator

CELMN-CD-NO

17 Mar 95

MEMORANDUM THRU C/Const Div, ATTN: Contr Admin Br

FOR C/Contr Div

SUBJECT: Contract No. DACW29-94-C-0079, Lake Pontchartrain, LA and Vicinity, High Level Plan, London Avenue Outfall Canal, Parallel Protection, Mirabeau Avenue to Leon C. Simon Boulevard Floodwall

Modification P00006, CIN-02 to the subject contract is forwarded for the contract file.

Enclosure


CHESTER ASHLEY

Area Engineer
New Orleans Area Office

Ja

MAR 17 1995

AMENDMENT OF SOLICITATION/MODIFICATION OF CONTRACT

1. CONTRACT ID CODE
077

PAGE OF PAGES
1 2

2. AMENDMENT/MODIFICATION NO.
P00006

3. EFFECTIVE DATE
03/07/95

4. REQUISITION/PURCHASE REQ. NO.

5. PROJECT NO. (if applicable)
CIN-02

6. ISSUED BY
US ARMY ENGR DIST NEW ORLEANS
PO BOX 60267
NEW ORLEANS LA 70160-0267
Cynthia Whitten

CODE
SC5(504) 862-1899

7. ADMINISTERED BY (if other than Item 6)
CELMN-CT-CC MS. WHITTEN
PHONE: (504) 862-1899

CODE
modcw

8. NAME AND ADDRESS OF CONTRACTOR (No., street, county, State and ZIP Code) Vendor ID: 00001344

B&K CONSTRUCTION
1905 HIGHWAY 59
MANDEVILLE LA 70448

9A. AMENDMENT OF SOLICITATION NO.

9B. DATED (SEE ITEM 11)

10A. MODIFICATION OF CONTRACT/ORDER NO.
DACW29-94-C-0079

10B. DATED (SEE ITEM 13)
07/11/94

CODE
OGTN3

FACILITY CODE

11. THIS ITEM ONLY APPLIES TO AMENDMENTS OF SOLICITATIONS

The above numbered solicitation is amended as set forth in Item 14. The hour and date specified for receipt of Offers is extended, is not extended. Offers must acknowledge receipt of this amendment prior to the hour and date specified in the solicitation or as amended, by one of the following methods: (a) By completing Items 8 and 15, and returning _____ copies of the amendment; (b) By acknowledging receipt of this amendment on each copy of the offer submitted; or (c) By separate letter or telegram which includes a reference to the solicitation and amendment numbers. FAILURE OF YOUR ACKNOWLEDGMENT TO BE RECEIVED AT THE PLACE DESIGNATED FOR THE RECEIPT OF OFFERS PRIOR TO THE HOUR AND DATE SPECIFIED MAY RESULT IN REJECTION OF YOUR OFFER. If by virtue of this amendment you desire to change an offer already submitted, such change may be made by telegram or letter, provided each telegram or letter makes reference to the solicitation and this amendment, and is received prior to the opening hour and date specified.

12. ACCOUNTING AND APPROPRIATION DATA (if required)

Mod Obligated Amount US \$9,263.77

Funds in the amount of \$9,263.77 are available. See Attached.

13. THIS ITEM APPLIES ONLY TO MODIFICATIONS OF CONTRACTS/ORDERS, IT MODIFIES THE CONTRACT/ORDER NO. AS DESCRIBED IN ITEM 14.

(X) A. THIS CHANGE ORDER IS ISSUED PURSUANT TO: (Specify authority) THE CHANGES SET FORTH IN ITEM 14 ARE MADE IN THE CONTRACT ORDER NO. IN ITEM 10A.
X CC 1.83 Changes

B. THE ABOVE NUMBERED CONTRACT/ORDER IS MODIFIED TO REFLECT THE ADMINISTRATIVE CHANGES (such as changes in paying office, appropriation date, etc.) SET FORTH IN ITEM 14, PURSUANT TO THE AUTHORITY OF FAR 43.103 (b).

C. THIS SUPPLEMENTAL AGREEMENT IS ENTERED INTO PURSUANT TO AUTHORITY OF:

D. OTHER (Specify type of modification and authority)

E. IMPORTANT: Contractor is not, is required to sign this document and return original copies to the issuing office.

14. DESCRIPTION OF AMENDMENT/MODIFICATION (Organized by UCF section headings, including solicitation/contract subject matter where feasible.)

The following change is made to the above numbered contract for Lake Pontchartrain, LA & Vicinity, HLP, London Avenue Outfall Canal, Parallel Protection, Mirabeau Avenue to Leon C. Simon Boulevard Floodwall, Orleans Parish, LA, to provide a wooden fence at the staging area.

Except as provided herein, all terms and conditions of the document referenced in Item 9A or 10A, as heretofore changed, remains unchanged and in full force and effect.

15A. NAME AND TITLE OF SIGNER (Type or print)
H. J. Keryon, President

15B. CONTRACTOR/OFFEROR
[Signature]
Signature of person authorized to sign

15C. DATE SIGNED
3/9/95

16A. NAME AND TITLE OF CONTRACTING OFFICER (Type or print)
Chester Ashley, ACO

16B. UNITED STATES OF AMERICA
BY *[Signature]*
Chester Ashley
(Signature of Contracting Officer)

16C. DATE SIGNED
3-10-95

SF 30 CONTINUATION SHEET

12. Accounting and Appropriation Data (Cont.)

96X8862 FWL2111000NOLML

14. Description of Amendment/Modification (Cont.)

CHANGES TO THE BIDDING SCHEDULE: The schedule of Contract Items, Descriptions, Estimated Quantities, Units, Unit Prices, and Estimated Amounts is modified as follows:

Item No.	Description	Estimated Quantity	Unit	Unit Price	Estimated Amount	Amount of Change
0022	Fencing (CIN-02)	LUMP SUM	LS	-----	\$9,263.77	(+) \$9,263.77

CHANGES TO THE CONTRACT SPECIFICATIONS: Add the following sentence to the end of paragraph C2F-1: "The work also consists of providing and installing a wooden fence fronting the field office, to obstruct the view of the staging area by the residents located directly across the street."

Add new paragraph C2F-5.1 as follows: "C2F-5.1. MEASUREMENT AND PAYMENT. (CIN-02). Work for providing and installing a wooden fence at the field office will not be measured for payment. Payment for the wooden fence will be made at the lump sum price for "Fencing (CIN-02)." Price and payment shall include all costs for providing and installing the wooden fence and for all costs associated with the return and restocking of the privacy slats."

CHANGES TO THE CONTRACT DRAWINGS: There are no changes to the contract drawings.

CHANGES TO THE CONTRACT PRICE: The contract price is increased by \$9,263.77.

CHANGES TO THE CONTRACT TIME: The contract time remains unchanged.

It is further understood and agreed that this adjustment constitutes compensation in full on behalf of the contractor, its subcontractors and suppliers for all costs and markups directly or indirectly attributable to the changes ordered for all delays, impacts, and extended overhead related thereto, and for performance of the change within the time frame stated.



DEPARTMENT OF THE ARMY

NEW ORLEANS DISTRICT, CORPS OF ENGINEERS

P.O. BOX 60267

NEW ORLEANS, LOUISIANA 70160-0267

REPLY TO
ATTENTION OF:

MAR 12 1985

Construction Division
New Orleans Area Office

B&K Construction
1905 Highway 59
Mandeville, LA 70448

Gentlemen:

Enclosed for your file is the duplicate original of Modification P00006, CIN-02 for Contract No. DACW29-94-C-0079.

Sincerely,

Chester Ashley
Administrative Contracting
Officer

Enclosure

CW
WHITTEN
CELMN-CT-R

ASHLEY *CJ*
CELMN-CD-NO

CW
WHITTEN
CELMN-CT-R

Standard Form 30

GOINS
3/11/95
MORTON
3/2/95
DUTTON
WHITTEN

Block 5: CIN 02

Block 6: U.S. Army Engineer District, New Orleans
Corps of Engineers
P.O. Box 60267
New Orleans, LA 70160-0267

Block 8: B & K Construction Company, Incorporated
1905 Highway 59
Mandeville, LA 70448

Block 10A: DACW29-94-C-0079

Block 10B: 11 July 1994

Block 12: Funds in the amount of \$9,263.77 are available under
Appropriation 96X8862, Contributed Funds, Account No.
FWL21 1100 ON OLML.

Block 13: Check box 'A'. CC I.83 CHANGES
"X" in "is required" block
"ORIGINAL" in blank
line thru "copies"

Block 14: Description of modification.

The following change is made to the above numbered contract
for Lake Pontchartrain, Louisiana and Vicinity, High Level Plan,
London Avenue Outfffall Canal, Parallel Protection, Mirabeau
Avenue to Leon C. Simon Boulevard Floodwall, Orleans Parish,
Louisiana to provide a wooden fence at the staging area.

Changes to the Bidding Schedule: The schedule of Contract Items,
Descriptions, Estimated Quantities, Units, Unit Prices and
Estimated Amounts is modified by adding new bid items as follows:

Item No.	Description	Est Qty	Unit	Unit Price	Est Amt	Amount of Change
0022	Fencing (CIN-02)	L.S.	L.S.	-----	\$9,263.77	(+) \$9,263.77

Changes to the Contract Specifications: Add the following sentence to the
end of paragraph C2F-1.

"The work also consists of providing and installing a wooden fence fronting
the field office, to obstruct the view of the staging area by the residents
located directly across the street."

Add new paragraph C2F-5.1 as follows:

"C2F-5.1. MEASUREMENT AND PAYMENT (CIN 02). Work for providing and
installing wooden fence at the field office will not be measured for
payment. Payment for the wooden fence will be made at the lump sum price
for "Fencing (CIN-02)". Price and payment shall include all costs for

providing and installing the wooden fence and for all costs associated with the return and restocking of the privacy slats."

Changes to the Contract Drawings: There are no changes to the contract drawings.

Changes to the Contract Price: The contract price is increased by \$9,263.77.

Changes to the Contract Time: The contract time remains unchanged.

It is further understood and agreed that this adjustment constitutes compensation in full on behalf of the contractor, its subcontractors and suppliers for all costs and markups directly or indirectly attributable to the changes ordered, for all delays, impacts and extended overhead related thereto, and for performance of the change within the time frame stated.

Standard Form 30

SS GOINS
SSM 12/27 MORTON
D DUTTON
— WHITTEN

Block 5: CIN 02

Block 6: U.S. Army Engineer District, New Orleans
Corps of Engineers
P.O. Box 60267
New Orleans, LA 70160-0267

Block 8: B & K Construction Company, Incorporated
1905 Highway 59
Mandeville, LA 70448

Block 10A: DACW29-94-C-0079

Block 10B: 11 July 1994

Block 12: Funds in the amount of \$3,634.09 are available under
Appropriation 96X8862, Contributed Funds, Account No.
FWL21 1100 ON OLML.

Block 13: Check box 'A'. CC I.83 CHANGES
"X" in "is required" block
"ORIGINAL" in blank
line thru "copies"

Block 14: Description of modification.

The following change is made to the above numbered contract
for Lake Pontchartrain, Louisiana and Vicinity, High Level Plan,
London Avenue Outfffall Canal, Parallel Protection, Mirabeau
Avenue to Leon C. Simon Boulevard Floodwall, Orleans Parish,
Louisiana to provide slats in the existing chain link fence
around the field office, ~~located at 6201 Pratt Drive.~~

Changes to the Bidding Schedule: The schedule of Contract Items,
Descriptions, Estimated Quantities, Units, Unit Prices and
Estimated Amounts is modified by adding new bid items as follows:

Item No.	Description	Est Qty	Unit	Unit Price	Est Amt	Amount of Change
0022	Fencing Slats (CIN-02)	L.S.	L.S.	-----	\$3,634.09	(+) \$3,634.09

Changes to the Contract Specifications: Add the following sentence to the
end of paragraph C2F-1.

"The work also consists of providing slats for the fence fronting the field
office, to obstruct the view of the staging area by the residents located
directly across the street."

Add new paragraph C2F-5.1 as follows:

"C2F-5.1. MEASUREMENT AND PAYMENT (CIN 02). Work for providing and
installing privacy slats in the existing chain link fence at the field
office will not be measured for payment. Payment for the privacy slats

will be made at the lump sum price for "Fencing Slats (CIN-02)". Price and payment shall include all costs for providing and installing the privacy slats."

Changes to the Contract Drawings: There are no changes to the contract drawings.

Changes to the Contract Price: The contract price is increased by \$3,634.09.

Changes to the Contract Time: The contract time remains unchanged.

It is further understood and agreed that this adjustment constitutes compensation in full on behalf of the contractor, its subcontractors and suppliers for all costs and markups directly or indirectly attributable to the changes ordered, for all delays, impacts and extended overhead related thereto, and for performance of the change within the time frame stated.

PRICE NEGOTIATION MEMORANDUM

Lake Ponchartrain, Louisiana and Vicinity,
High Level Plan,
London Avenue Outfall Canal,
Parallel Protection,
Mirabeau Avenue to Leon C. Simon Boulevard Floodawall,
Orleans Parish, Louisiana
Contract Number DACW29-94-C-0079, CIN 02
B & K Construction Co., Inc.

1. CONTRACT DESCRIPTION. The subject contract was awarded on 11 July 1994 in the amount of \$4,554,500.00. The contract consists of clearing and grubbing, selective demolition, demolition of a pedestrian bridge, structural excavation and backfill, fertilizing seeding, and mulching, cutting existing sheet piling, pulling existing sheet piling, redriving existing sheet piling, providing and installing new sheet piling, painting, constructing reinforced concrete floodwalls, constructing concrete slope pavement, utility modifications, relocation of feeder lines, erosion control, and temporary flood protection and cofferdams.

2. DESCRIPTION OF MODIFICATION.

a. SUMMARY AND NECESSITY FOR CHANGE. The user, the Orleans Levee District, requested slats be added to the fencing to obstruct the view of the staging area by the residents directly across the street.

b. REASON FOR OMISSION FROM PLANS AND SPECIFICATIONS. It was realized subsequent to award at the request of the Orleans Levee District.

c. AUTHORITY FOR MODIFICATION: This change is issued under the authority provided by Contract Clause I.83 Changes.

3. PRICE AND TIME JUSTIFICATION:

a. SUMMARY.

<u>Contractor Proposal</u>	<u>Government Estimate</u>	<u>Negotiated Settlement</u>
\$3,634.09	\$5,288.69	\$3,634.09

b. PRICING STRATEGY. A price analysis was used to evaluate the contractor's proposal using independent Government Estimates which were prepared based on site specific resources and standard industry practices.


c. Participants. Mr. Mike Tassin was the Lead Negotiator for B & K Construction Co., Inc., and Mr. Stradford Goins was the Lead Negotiator for the Government.

d. NEGOTIATION SUMMARY. By verbal request on 16 November 1994 the Government requested a proposal from the contractor to add slats to the fencing around the field office to obstruct the view of the staging area by the residents directly across the street. An independent Government estimate was prepared on 18 November 1994 in the amount of \$5,288.69. The contractor proposal was received on 1 December 1994 in the amount of \$3,634.09. On 2 December 1994, via telephone, the contractor was informed that his proposal in the amount of \$3,634.09 compared favorably to the government estimate and was considered to be fair and reasonable and was accepted. The contractor also agreed that this modification eliminated all impacts to the contract as a result of this change and that the contract time be remained unchanged.

4. APPROPRIATION DATA. Funds in the amount of \$3,634.09 are available under Appropriation 96X8862, Contributed Funds, Account No. FWL21 1100 ON OLML, Accounting Element 284.

SUBMITTED FOR APPROVAL

Date: 12 December 1994


STRADFORD GOINS
Lead Government Negotiator

MODIFICATION PACKAGE INDEX

Contract Number: 94-C-0079 CIN: CIN 2

Description of Change: Slats for Fence

Office Engineer: GOINS

ITEM	DOCUMENT	DATE	INITIALS	REMARKS
1	Request for Change from User/Engr Div	_____	_____	N/A
2	Unpriced Change Order with Memo and SF30 NTP	_____	_____	_____
3	Correspondence	9 Nov 94	JS	User (OLD) request
4	Request for Proposal	16 Nov 94	JS	verbal request
5	Government Estimate or Worksheet	18 Nov 94	JS	
6	Contractor's Proposal	1 Dec 94	JS	
7	Funds Availability Statement	12/20/94	JS	
8	Standard Form 30	12/27/94		DRAFT
9	Post Negotiation Memorandum			

NOTE: ITEMS LISTED ARE PERFORMED AS REQUIRED AND THE LISTING SHOWN DOES NOT INDICATE A SET SEQUENCE TO BE FOLLOWED.

Review of DRAFT 12/27 JS 3/1/95 JS
 TO Contracting 12/27/94 TO 3/2/95

Returned 1/4/95
 Dennis called from the jobsite on 1/4/95 to inform me he can see right through the slats that the contractor started to install. He is going to tell the contractor to put up something that works and we are going to put the mod on hold. JS

CHANGE REQUEST

CIN 02

CONTRACT NO. 94-C-0079 DATE: 1/12/95
 TITLE/LOCATION: Lake Pontchartrain & Vic. Hur. Prot. London Ave Canal Paralled Protection
 TO: CELMN-PP FROM (POC): Jim Berry X1240

1. DESCRIPTION OF CHANGE (INCLUDE PLANS, SPECS, & REFERENCES):
Install wooden in lieu of chain link fence in the staging area. This revises the slats in the chain link fence
2. REASON FOR CHANGE:
Locals in the area did not want to look at the port a lets in the staging area.
3. AUTHORITY FOR CHANGE: Changes Clause
4. DATE CHANGE DISCOVERED: 15 Nov 94
5. DESIGN ASSISTANCE REQUIRED:
6. ESTIMATED COST: 9,311.94 ESTIMATED TIME:
7. COMMENTS/REMARKS: New Orleans Levee District to pay 100%
8. STATUS OF FUNDS: 3,634.09 previously committed
9. CONST. MGR./DATE: Jim Berry 1/12/95 CHG. CAT. C4

FUNDING REQUEST

1. Please Program and Commit \$ 5,677.85 for 2nd QTR, FY 95
2. Estimated total contract amount is \$ 4,578,816.13 ORG CODE: VD
3. Accounting Data: 96X8862 FWL211100 ONOLML ACCT.ELEMENT284

DISTRIBUTION	APPROVAL	DATE	FUNDING STAMP
PROJECT MANAGER (Program Funds)	<u>[C. Ritter]</u>	<u>2-14-95</u>	Date <u>2/23/95</u> Funds Available: <u>#5,677.85</u> Appropriation: <u>96X8862</u> <input checked="" type="checkbox"/> Committed, F & A Obligated for Brenda Weber, F & A Officer <u>[Signature]</u> Accounts Clerk
PP-P (Certify Funds)	<u>D. Hurn</u>	<u>2/14/95</u>	
F&A (Commit Funds)	<u>L. Butler</u>	<u>2/23/95</u>	

Judy Uem X2944
 Program Analyst, POC

[Signature]
 Chief, Construction Division/ Date
 RICHARD T. HILL

CF: CELMN-CD-~~LS~~/NO
 CELMN-PP/~~OB~~/ED

CELMN-PP-P
~~CELMN-CD-CH~~ CELMN-CD-CCCS (BERRY)

CONTRACT NO. 94-C-0079 DATE: 11/21/94

TITLE/LOCATION: Lake Pontchartrre Huron Proj. London Ave Canal Parallel Protection

TO: CELMN-PP FROM (POC): Jim Berry

1. DESCRIPTION OF CHANGE (INCLUDE PLANS, SPECS, & REFERENCES):

Place Slats in The chain link fence surrounding the staging area.

2. REASON FOR CHANGE:

Locals in the area did not want to look at the porta lets.

3. AUTHORITY FOR CHANGE: Changes Clause

4. DATE CHANGE DISCOVERED: 15 Nov 94

5. DESIGN ASSISTANCE REQUIRED: —

6. ESTIMATED COST: \$5,000 ^{\$3,634.09} ESTIMATED TIME: 0

7. COMMENTS/REMARKS: New Orleans levee district to pay 100%

8. STATUS OF FUNDS: —

9. CONST. MGR./DATE: Jim Berry 11/21/94 CHG. CAT. CA

FUNDING REQUEST

- 1. Please Program and Commit \$ 5,000.00 ^{\$3,634.09} for 1st QTR, FY 95
- 2. Estimated total contract amount is \$ 4,629,500.00 ORG CODE: VD
- 3. Accounting Data: FWL21 11 00 ON OLML 4,628,134.09 Acctng Element 284
FWL21 11 00 ON OLML

DISTRIBUTION	APPROVAL	DATE	FUNDING STAMP
PROJECT MANAGER (Program Funds)	<u>[Signature]</u>	<u>11/29/94</u>	Date <u>11/24/94</u> Funds Available: <u>3634.09</u> Ap. # <u>96 X 8862</u> <input checked="" type="checkbox"/> Obligated <input type="checkbox"/> Obligated For Release With: F & A Officer <u>[Signature]</u> In Charge Accounts Clerk
PP-P (Certify Funds)	<u>A. Lumm</u>	<u>12/1/94</u>	
F&A (Commit Funds)	<u>[Signature]</u>	<u>12/2/94</u>	

Judy Ulm X 294
Program Analyst, POC

[Signature]
Chief, Construction Division/ Date
RICHARD T. HILL

CF: CELMN-CD-~~EA~~/NO CELMN-PP-P
CELMN-PP/~~OH/ED~~ CELMN-CD-~~CK~~ CELMN-CD-CC (BERRY)

Worksheet

DACW29-94-C-0079, CIN 02

Provide and Wood Fencing:

Quote from Westside Fence 560 feet @ \$10.00	=	\$5,600.00
Installation and Removal of Slats	=	\$266.00
Restock Slats	=	\$300.33
Freight for Returning Slats	=	\$448.00
SUBTOTAL	=	\$6,614.33
SUB(OH)10%	=	\$661.43
SUBTOTAL	=	\$7,275.76
PROFIT (SUB) 8%	=	\$582.06
SUBTOTAL	=	\$7,857.82
FOOH	=	\$ 0.00
SUBTOTAL	=	\$7,857.82
HOOH 10%	=	\$ 785.78
SUBTOTAL	=	\$8,643.60
PROFIT 6%	=	\$ 518.62
SUBTOTAL	=	\$9,162.22
<i>gr actual = 1.5%</i> BOND 1%	=	\$ 91.62 137.43 <i>gr</i>
TOTAL	=	\$9,253.84 9299.65 <i>gr</i>

Stradford Goins
Stradford Goins
1/13/95
Date

FROM:

PHONE NO. :

P01



Ace Fence Company

"By the foot or by the mile"

418 E. Josephine Street
P.O. Box 1298
Chalmette, LA 70044
(504) 279-4487
Fax (504) 279-1488

FACSIMILE TRANSMISSION
From: David Farrar
1 Page(s)

TO : B&K Construction
Attn: Debbie

DATE : January 6, 1995

FAX PHONE : 504-626-9710

SUBJECT : Fence Slats Pratt Drive

The following is a list of my costs involved in the project on Pratt Drive.

1	Installation and removal of 44 ft. fence slat material. This material is non returnable to our supplier.	\$266
2	- Re-stocking fee from our supplier on unused material.	\$300.33
3	Freight charge to return 800lbs unused material to Hicksville, NY @ \$56 per 100lbs. Yellow or Consolidated Freight Companies.	\$448.00
	Our Total Cost	----- \$1014.00

Ace will be meeting with the Engineers this morning to develop a new plan of action. We will work with you any way we can. Please call if you have any questions.

Thank You,

David

FROM :

PHONE NO. :

P02

FENCING ESTIMATES AND PROPOSAL

279-4488

ACE FENCE COMPANY

USACOF

"By the foot or by the mile"

418 E. JOSEPHINE
P.O. BOX 1298
CHALMETTE, LA 70043
PHONE 279-4487

Customer's Name

R 62-1246

Address

Fox 862-1226

City

State

Phone

Mr. Standard

Goins

Fed. I-D# 721162929

Date: 1-5-95


SPECIFICATIONS AND MATERIALS

Type	Overall Height	Mesh & Gauge of Wire	Settings	Outside Diameter Live Posts	Line Post Spacing	Outside Diameter Top Rail	Outside Diameter Gate Rail
wood	72			curb		2x4	2x4

Quantity	Description	Unit	Quantity	Description	Unit
_____	Lineal Feet Complete Fence	_____	_____	Drive Gates	_____
_____	Lineal Feet Complete Fence	_____	_____	Drive Gates	_____
_____	Walk Gates	_____	_____	End Posts	_____ O.D.
_____	Walk Gates	_____	_____	End Posts	_____ O.D.
_____		_____	_____	Corner Posts	_____ O.D.
_____		_____	_____	Corner Posts	_____ O.D.
_____		_____	_____	Gate Posts	_____ O.D.
_____		_____	_____	Gate Posts	_____ O.D.

Location of Property on which Fence is to be erected

(Property Size)

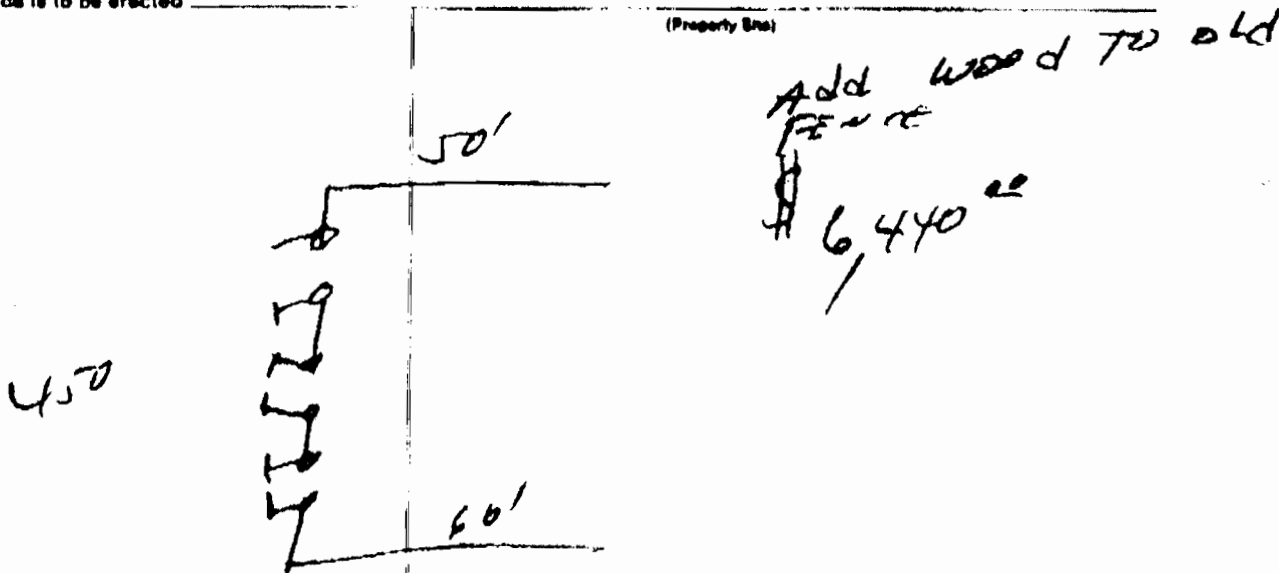

Not responsible for underground wires and pipes.

You, as the property owner are solely responsible for locating property line. We do not survey your property or remove trees or shrubs.

The undersigned customer assumes full responsibility for the location of the line upon which said fence material is to be installed and agrees to hold ACE FENCE harmless from all claims arising from questions of survey of said property or location of said line.

Should it be necessary to employ an attorney to collect the said amount of this purchase, Purchaser agrees to pay all attorney's fees and costs to do so, or 33-1/3 percent.

This contract price is due on completion, by cash or by finance. Specification and proposal valid upon approval of designer.

ACE FENCE COMPANY

APPROVED AND ACCEPTED:

- Cash
- POC
- Financing

By: *[Signature]*

SUBCONTRACTS:

		Rate	Unit	Total
ACE FENCE COMPANY	Remove panel weave	1,014.00	1.00	1,014.00
	Add wood to chain link fence	6,440.00	1.00	6,440.00
TOTAL SUBCONTRACT				7,454.00

TOTAL COSTS SUMMARY

LABOR	151.15
EQUIPMENT	0.00
MATERIALS	0.00
SUBCONTRACTS	7,454.00

TOTAL	7,605.15

OVERHEAD/PROFIT


G & A	13.90%	1,057.12
	SUBTOTAL	8,662.27
PROFIT	7.50%	649.67

=====

TOTAL COST	9,311.94
------------	----------

=====

9402\RFC002A.SS



CONSTRUCTION COMPANY, INC.

January 11, 1995

Mr. Stradford Goins
U.S. Army Corps of Engineers
New Orleans District
P. O. Box 60167
New Orleans, LA 70160-0267

RE: LONDON AVENUE OUTFALL CANAL
CONTRACT NO. DACW29-94-C-0079
U.S. ARMY CORPS OF ENGINEERS
B & K JOB NO. 9402
Request for Change No. 002A

Dear Mr. Goins,

We have enclosed our revised price of \$9,311.94 to install 560 LF of wood fence to the existing chain link fence at the field office location of 6201 Pratt Drive.

In this breakdown, we have included the cost incurred in the partial installation of the privacy slats which were to be installed at this site. The wood fencing will allow 100% coverage as indicated by Mr. Ace of Ace Fence Company.

If you need additional information, please do not hesitate to call.

Sincerely,
B & K CONSTRUCTION CO., INC.

Deborah W. Smith
Project Coordinator

DWS/lw
Enclosures

cc: Mr. Chester Ashley, Contracting Officer
Mr. Mike Tassin, Field Superintendent
Mr. Ace, Ace Fence Company

\9404\RFC#2A


CONTRACT DACW24-94-C-0079
 LAKE PONTCHARTRAIN AND VICINITY
 HIGH LEVEL PLAN, LONDON AVENUE
 OUTFALL CANAL, PARALLEL PROTECTION
 LEON C. SIMON BLVD. FLOODWALL
 ORLEANS PARISH, LOUISIANA
 B & K JOB NO. 9402, RFC NO. 002A
 January 11, 1995

DESCRIPTION: COE requested price to remove panel weave privacy slats from and add wood to existing chain link fence.

LABOR	Name	Rate	Rg Hrs	OT Hrs	Total
				0.00	0.00
(Superintendent)	Mike Tassin	22.50	2.50	0.00	56.25
(Project Coord.)	Deborah Smith	15.00	2.50	0.00	37.50
(Clerk)	Margaret Williams	7.50	0.50	0.00	3.75
Sub Total					97.50
PR Tax & Ins @	55.03%				53.65
					0.00
TOTAL LABOR					151.15

EQUIPMENT	Description	Rate	Hours	Total
				0.00
				0.00
				0.00
				0.00
TOTAL EQUIPMENT				0.00

MATERIALS	Description	Price	Qty	Total
				0.00
				0.00
				0.00
Sub Total				0.00
Tax @	9.00%			0.00
TOTAL MATERIALS				0.00



CONSTRUCTION COMPANY, INC

F A X C O V E R M E M O

TO: NAME: Stradford Hoins
 COMPANY: U.S. Army Corps of Engineers
 PHONE: _____ FAX: 862-1226

FROM: NAME: Debbie Smith
 DATE: 1-11-95

REFERENCE: RFC #002A

NUMBER OF PAGES INCLUDING THIS SHEET: 6

ORIGINAL TO FOLLOW BY MAIL:
 YES X NO _____ UPON REQUEST _____

ACE FENCE COMPANY

"By the foot or by the mile"

418 E. JOSEPHINE
P.O. BOX 1298
CHALMETTE, LA 70043
PHONE 279-4487

USACOF

Customer's Name 862 1246

Address FA 862 1226

City State Phone

Mr Strandford
60105

Date 1-5-95


Fed. I-D# 721152929

SPECIFICATIONS AND MATERIALS

Type	Overall Height	Mesh & Gauge of Wire	Sealage	Outside Diameter Line Posts	Line Post Spacing	Outside Diameter Top Rail	Outside Diameter Gate PR
Rib	6			2 1/2	8'		2x1
PANEL							closure
Quantity		Quantity		Size	Quantity		Size
524	Linear Feet Complete Fence	3	Drive Gates	12'x6"		Corner Posts	O.D.
	Linear Feet Complete Fence		Drive Gates			Corner Posts	O.D.
	Walk Gates		End Posts	O.D.		Gate Posts	O.D.
	Walk Gates		End Posts	O.D.		Gate Posts	O.D.

Location of Property on which Fence is to be erected

(Property Site)

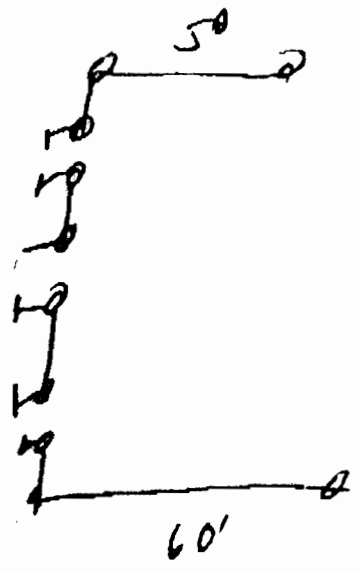

NEW FENCE
100% Privacy
\$10,108⁰⁰

Option: Remove 01
Fence - 50%

Not responsible for underground wires and pipes

You, as the property owner are solely responsible for locating property line. We do not survey your property or remove trees or shrubs.

The undersigned customer assumes full responsibility for the location of the line upon which said fence material is to be installed and agrees to hold ACE FENCE harmless from all claims arising from questions of survey of said property or location of said line.

Should it be necessary to employ an attorney to collect the said amount of this purchase, Purchaser agrees to pay all attorney's fees and costs to do so, or 33-1/3 percent.

This contract price is due on completion, by cash or by finance. Specification and proposal valid upon approval of designer.

ACE FENCE COMPANY

APPROVED AND ACCEPTED:

- Cash
- POC
- Financing

By *[Signature]*
(Sales Representative)

(Customer's Signature)

FENCING ESTIMATES AND PROPOSAL

279-4487

279-4488

ACE FENCE COMPANY

USACOF

"By the foot or by the mile"

418 E. JOSEPHINE
P.O. BOX 1298
CHALMETTE, LA 70043
PHONE 279-4487

Customer's Name

862-1246

Address

Fat 862-1226

City

State

Phone

Mr. Standard

Goins

Date

1-5-95

Fed. I-D# 721152929


SPECIFICATIONS AND MATERIALS

Type	Overall Height	Mesh & Gauge of Wire	Spacing	Outside Diameter Line Posts	Line Post Spacing	Outside Diameter Top Rail	Outside Diameter Gate RA
wood	72			Custom		2x4	2x4

Quantity	Quantity	Size	Quantity	Size
Lineal Feet Complete Fence	Drive Gates		Corner Posts	O.D.
Lineal Feet Complete Fence	Drive Gates		Corner Posts	O.D.
Walk Gates	End Posts	O.D.	Gate Posts	O.D.
Walk Gates	End Posts	O.D.	Gate Posts	O.D.

Location of Property on which Fence is to be erected

(Property Site)

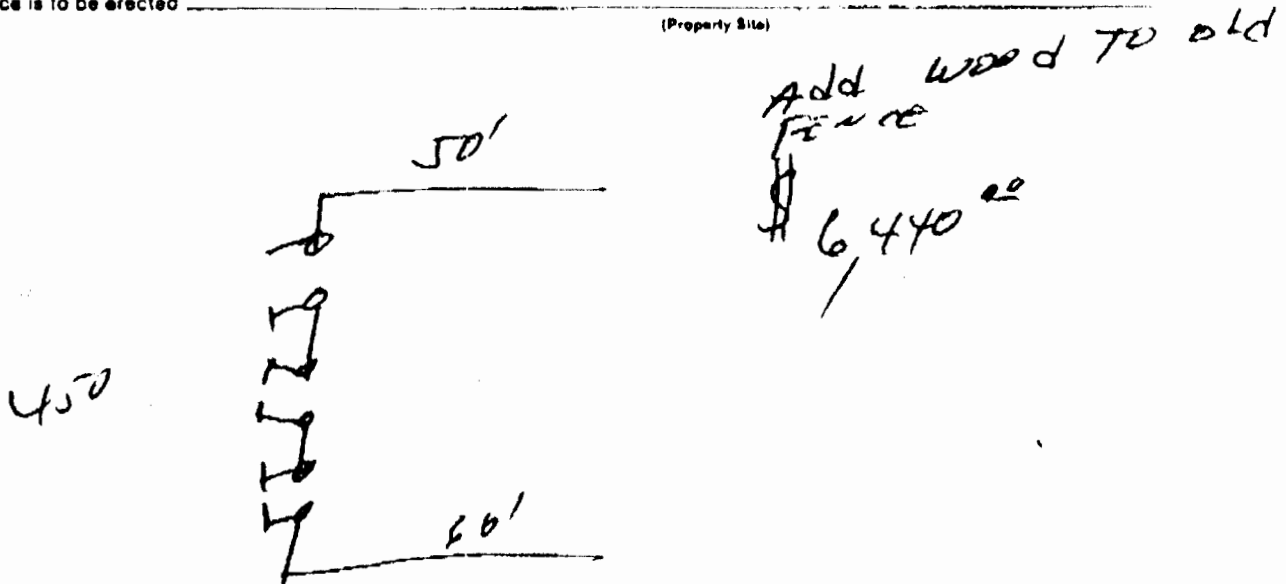

Not responsible for underground wires and pipes.
 You as the property owner are solely responsible for locating property line. We do not survey your property or remove trees or shrubs.
 The undersigned customer assumes full responsibility for the location of the line upon which said fence material is to be installed and agrees to hold ACE FENCE harmless from all claims arising from questions of survey of said property or location of said line.
 Should it be necessary to employ an attorney to collect the said amount of this purchase, Purchaser agrees to pay all attorney's fees and costs to do so, or 33-1/3 percent.
 This contract price is due on completion, by cash or by finance.
 Specification and proposal valid upon approval of designer.

APPROVED AND ACCEPTED:

- Cash
- POC
- Financing

ACE FENCE COMPANY

By John L. By
Sales Representative

(Customer's Signature)

ROUTING SLIP - ACTION/SUSPENSE COPY
 - SUSPENSE DATE:

CELMN-CD-NO	INITIAL	DATE
ASHLEY		
BERNARD		
HABBAZ		
TUCKER		
SMITH		
ADAMS		

CELMN-CD-NO-E - OFFICE ENGINEER

MORTON		
PEREZ		
GOINS		
URBAN		
BRUNO		
HAGAN		
BLACKSTOCK		

CELMN-CD-NO-Q - LWR MISS RIVER & NO - VEN HP

FOGARTY		
BOURGEOIS		
DAVIS, D.		
CARR		
BLANCHARD		

CELMN-CD-NO-Q - LAKE PONT & CHAL AREA HP

DUHON		11/3/95
BOUDREAU		
WAGNER		
DAVIS, A.		
GONZALES		

CELMN-CD-NO-Q - BY BONFOUCA RES OFC

MORGAN		
MONTGUT		
BRAKEL		
SHERMAN		
SMALLWOOD		

CELMN-CD-NO-Q - SWP & VICINITY

HINKAMP		
BURGESS, C.		
DERBES		
HARTLEY		
HUTSON		
SCARABIN		

CELMN-CD-NO-Q - UPR MISS RIVER & W JEFF HP

TILLY		
CRUMHOLT		
LAUTO		

CONST DIV, CONST MGMT SEC
 (FOR THE CONTRACT FILE)

NOAO FILE

REMARKS:



CONSTRUCTION COMPANY, INC.

January 11, 1995

Mr. Stradford Goins
U.S. Army Corps of Engineers
New Orleans District
P. O. Box 60167
New Orleans, LA 70160-0267

RE: LONDON AVENUE OUTFALL CANAL
CONTRACT NO. DACW29-94-C-0079
U.S. ARMY CORPS OF ENGINEERS
B & K JOB NO. 9402
Request for Change No. 002A

Dear Mr. Goins,

We have enclosed our revised price of \$9,311.94 to install 560 LF of wood fence to the existing chain link fence at the field office location of 6201 Pratt Drive.

In this breakdown, we have included the cost incurred in the partial installation of the privacy slats which were to be installed at this site. The wood fencing will allow 100% coverage as indicated by Mr. Ace of Ace Fence Company.

If you need additional information, please do not hesitate to call.

Sincerely,
B & K CONSTRUCTION CO., INC.

Deborah W. Smith
Project Coordinator

DWS/lw
Enclosures

cc: Mr. Chester Ashley, Contracting Officer
Mr. Mike Tassin, Field Superintendent
Mr. Ace, Ace Fence Company

\9404\RFC#2A

JAN 13 1995
M. O. A. C.

CONTRACT DACW29-94-C-0079
 LAKE PONTCHARTRAIN AND VICINITY
 HIGH LEVEL PLAN, LONDON AVENUE
 OUTFALL CANAL, PARALLEL PROTECTION
 LEON C. SIMON BLVD. FLOODWALL
 ORLEANS PARISH, LOUISIANA
 B & K JOB NO. 9402, RFC NO. 002A
 January 11, 1995

DESCRIPTION: COE requested price to remove panel weave privacy slats from and add wood to existing chain link fence.

LABOR	Name	Rate	Rg Hrs	OT Hrs	Total
				0.00	0.00
(Superintendent)	Mike Tassin	22.50	2.50	0.00	56.25
(Project Coord.)	Deborah Smith	15.00	2.50	0.00	37.50
(Clerk)	Margaret Williams	7.50	0.50	0.00	3.75
Sub Total					97.50
PR Tax & Ins @	55.03%				53.65
					0.00
TOTAL LABOR					151.15

EQUIPMENT	Description	Rate	Hours	Total
				0.00
				0.00
				0.00
				0.00
TOTAL EQUIPMENT				0.00

MATERIALS	Description	Price	Qty	Total
				0.00
				0.00
				0.00
Sub Total				0.00
Tax @	9.00%			0.00
TOTAL MATERIALS				0.00

SUBCONTRACTS:		Rate	Unit	Total
ACE FENCE COMPANY	Remove panel weave	1,014.00	1.00	1,014.00
	Add wood to chain link fence	6,440.00	1.00	6,440.00
TOTAL SUBCONTRACT				7,454.00

TOTAL COSTS SUMMARY

LABOR	151.15
EQUIPMENT	0.00
MATERIALS	0.00
SUBCONTRACTS	7,454.00

TOTAL	7,605.15

OVERHEAD/PROFIT

G & A	13.90%	1,057.12
	SUBTOTAL	8,662.27
PROFIT	7.50%	649.67

=====	=====	=====
TOTAL COST		9,311.94
=====	=====	=====

9402\RFC002A.SS

279-4487

279-4488

FENCING ESTIMATES AND PROPOSAL

ACE FENCE COMPANY

USACOF

"By the foot or by the mile"

418 E. JOSEPHINE
P.O. BOX 1298
CHALMETTE, LA 70043
PHONE 279-4487

Customer's Name

R 62-1246

Address

Faf R 62-1226

City

State

Phone

Mr. Standard

Goins

Date

1-5-95

Fed. I-D# 721152929

SPECIFICATIONS AND MATERIALS

Type	Overall Height	Mesh & Gauge of Wire	Sealings	Outside Diameter Line Posts	Line Post Spacing	Outside Diameter Top Rail	Outside Diameter Gate Post
wood	72			Custom		2x4	2x4

Quantity

Quantity

Size

Quantity

Size

Lineal Feet Complete Fence

Drive Gates

Corner Posts

O.D.

Lineal Feet Complete Fence

Drive Gates

Corner Posts

O.D.

Walk Gates

End Posts

O.D.

Gate Posts

O.D.

Walk Gates

End Posts


O.D.

Gate Posts

O.D.

Location of Property on which Fence is to be erected

(Property Site)

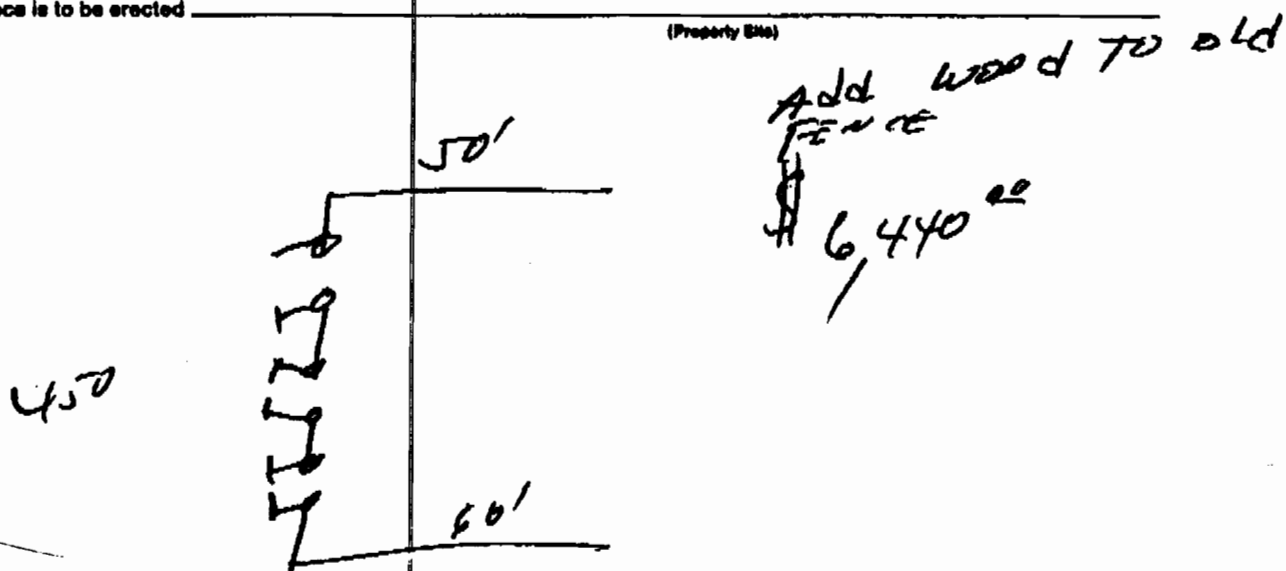

Not responsible for underground wires and pipes.

You, as the property owner are solely responsible for locating property line. We do not survey your property or remove trees or shrubs.

The undersigned customer assumes full responsibility for the location of the line upon which said fence material is to be installed and agrees to hold ACE FENCE harmless from all claims arising from questions of survey of said property or location of said line.

Should it be necessary to employ an attorney to collect the said amount of this purchase. Purchaser agrees to pay all attorney's fees and costs to do so, or 33-1/3 percent.

This contract price is due on completion, by cash or by finance. Specification and proposal valid upon approval of designer.

APPROVED AND ACCEPTED:

- Cash
- POC
- Financing

ACE FENCE COMPANY

By: Julia L. [Signature]
 (Sales Representative)

[Signature]

(Customer's Signature)



Ace Fence Company

"By the foot or by the mile"

418 F. Josephine Street
P.O. Box 1298
Chalmette, LA 70044
(504) 279-4487
Fax (504) 279-4488

FACSIMILE TRANSMISSION

From: David Farrar
1 Page(s)

TO : B&K Construction
Attn: Debbie

DATE : January 6, 1995

FAX PHONE : 504-626-9710

SUBJECT : Fence Slats Pratt Drive

The following is a list of my costs involved in the project on Pratt Drive.

- | | |
|--|----------|
| 1 - Installation and removal of 44 ft. fence slat material.
This material is non returnable to our supplier. | \$266 |
| 2 - Re-stocking fee from our supplier on unused material. | \$300.33 |
| 3 - Freight charge to return 800lbs unused material to
Hicksville, NY @ \$56 per 100lbs. Yellow or Consolidated
Freight Companies. | \$448.00 |

Our Total Cost -----
\$1014.00

Ace will be meeting with the Engineers this morning to develop a new plan of action. We will work with you any way we can. Please call if you have any questions.

Thank You,

David

Gov Est.

Acme Fence \$80/box (1 box = 10 L.F.)

$$510/10 = 51 \text{ boxes} \times \frac{\$80}{\text{box}} = 4080.00$$

9% tax 367.20

Subtotal 4447.20

OH 10% 444.72

Subtotal 4891.92

Profit 7% 342.43

Subtotal 5234.35

Bond 1% 52.34
\$5288.69

Stanford Gools

Nov 16, 1994

ROUTING SLIP - ACTION/SUSPENSE COPY
 - SUSPENSE DATE:

CELMN-CD-NO	INITIAL	DATE
ASHLEY		
BERNARD	<i>RB</i>	
HABBAZ		
TUCKER		
SMITH		
ADAMS		

CELMN-CD-NO-E - OFFICE ENGINEER

MORTON		
PEREZ		
GOINS	<i>A</i>	
URBAN		
BRUNO		
HAGAN		
BLACKSTOCK		

CELMN-CD-NO-Q - LWR MISS RIVER & NO - VEN HP

FOGARTY		
BOURGEOIS		
DAVIS, D.		
CARR		
BLANCHARD		

CELMN-CD-NO-Q - LAKE PONT & CHAL AREA HP

DUHON		
BOUDREAUX		
WAGNER		
DAVIS, A.		
GONZALES		

CELMN-CD-NO-Q - BY BONFOUCA RES OFC

MORGAN		
MONTEGUT		
BRAKEL		
SHERMAN		
SMALLWOOD		

CELMN-CD-NO-Q - SWP & VICINITY

HINKAMP		
BURGESS, C.		
DERBES		
HARTLEY		
HUTSON		
SCARABIN		

CELMN-CD-NO-Q - UPR MISS RIVER & W JEFF HP

TILLY		
CRUMHOLT		
LAUTO		

CONST DIV, CONST MGMT SEC
 (FOR THE CONTRACT FILE)

NOAO FILE

REMARKS:



CONSTRUCTION COMPANY, INC.

November 29, 1994

Mr. Stradford Goins
U.S. Army Corps of Engineers
New Orleans District
P.O. Box 60167
New Orleans, LA 70160-0267

RE: CONTRACT NO. DACW29-94-C-0079
LAKE PONTCHARTRAIN & VICINITY
HIGH LEVEL PLAN, LONDON AVENUE
OUTFALL CANAL, PARALLEL PROTECTION
MIRABEAU AVE TO LEON C. SIMON BLVD
FLOODWALL - ORLEANS PARISH, LA
B & K JOB NO. 9402
REQUEST FOR CHANGE NO. 002

Gentlemen:

We have enclosed our price of \$3,634.09 to install privacy slats in the existing chain link fence at our field office at 6201 Pratt Drive. We have quoted a fence which allows for 71% coverage. There are other types of slats which provide more coverage however the wind loading of these other types of fences are too great for the type of fence installed and could create some problems.

If you would like for us to quote some other type of fence please let us know and should you have any questions please do not hesitate to contact this office.

Sincerely,
B & K CONSTRUCTION CO., INC.


H. B. Kenyon,
President

HBK/kl
Enclosures

cc: Mr. Chester Ashley, Contracting Officer
Mr. Mike Tassin

9402/RFC2

CONTRACT DACW29-94-C-0079
 LAKE PONTCHARTRAIN AND VICINITY
 HIGH LEVEL PLAN, LONDON AVENUE
 OUTFALL CANAL, PARALLEL PROTECTION
 LEON C. SIMON BLVD. FLOODWALL
 ORLEANS PARISH, LOUISIANA
 B & K JOB NO. 9402, RFC NO. 002
 November 29, 1994

DESCRIPTION: COE requested price to panel weave privacy
 slats to existing chain link fence.

		Rate	Unit	Total
SUBCONTRACTS:				
ACE FENCE	Plastic privacy slats installed	2,968.00	1.00	2,968.00
OVERHEAD/PROFIT	G & A		13.90%	412.55
	SUBTOTAL			3,380.55
	PROFIT		7.50%	253.54
TOTAL COST				3,634.09

9402\RFC002.SS



Ace Fence Company


"By the foot or by the mile"

418 E. Louisiana Street
P.O. Box 100
Chalmette, LA 70044
(504) 279-4187
Fax (504) 279-4188

To: Debbie
B+K Construction
626-9710

Panel Wave
Privacy Slats
to Existing C.F.
Fence

This type of fence slat gives you 71% coverage. There are other types of slats that provide more coverage, but your temporary fence will sag due to weight & wind resistance. These are plastic and come in the colors listed.

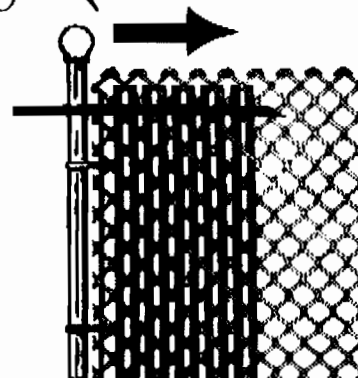

1. Slide a slat down vertically with locking tab on top.
2. Move locking strip horizontally to install one slat at a time.

FOURTH DIGIT OF PRODUCT CODE REPRESENTS

- | | |
|------------|-------------|
| 1 = Type V | 2 = Type Y |
| 3 = Type U | 4 = Type W |
| 5 = Type X | 6 = Type VS |

LAST DIGIT OF PRODUCT CODE REPRESENTS COLOR.

- | | | |
|-----------|------------|-------------|
| 0 = BLUE | 2 = SILVER | 3 = GRAY |
| 4 = BEIGE | 5 = GREEN | 6 = BLACK |
| 7 = BROWN | 8 = WHITE | 9 = REDWOOD |

510ft Slats Installed

\$ 2,968.⁰⁰

Please Call Me If You
Have Any Questions

Thank
Dee



CONSTRUCTION COMPANY, INC.

F A X C O V E R M E M O

TO: **NAME:** STRADFORD GOINS
COMPANY: U.S.A.C.O.E.
PHONE: _____ **FAX:** (504) 862-1226

FROM: **NAME:** Deborah Smith
DATE: 11/30/94

REFERENCE: LONDON AVENUE CANAL
REQUEST FOR CHANGE NO. 2 (PROPOSAL)
PRIVACY SLATS FOR EXISTING CHAIN LINK FENCE

NUMBER OF PAGES INCLUDING THIS SHEET: 4

ORIGINAL TO FOLLOW BY MAIL:
YES X **NO** _____ **UPON REQUEST** _____



Ace Fence Company

"By the fist or by the mile"

4115 Jambou Street
P.O. Box 1000


Chalmette, LA 70044
(504) 270-4187
Fax (504) 279-4188

To: Debbie

B+K Construction
626-9710

*Panel to go
Privacy Slats
to Existing F.C.H.
Fence*

This type of fence slat gives you 71% coverage. There are other types of slats that provide more coverage, but your temporary fence will sag due to weight & wind resistance. These are plastic and come in the colors listed.

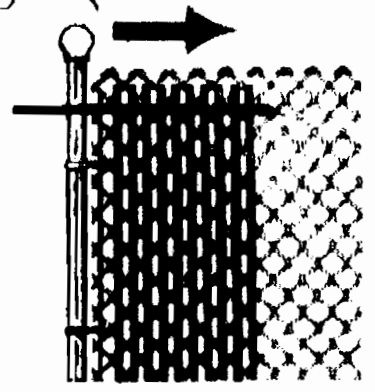

1. Slide a slat down vertically with locking tab on top
2. Move locking strip horizontally to install one slat at a time.

FOURTH DIGIT OF PRODUCT CODE REPRESENTS

- 1 = Type V 2 = Type Y
- 3 = Type U 4 = Type W
- 5 = Type X 6 = Type VS

LAST DIGIT OF PRODUCT CODE REPRESENTS COLOR

- 0 = BLUE 2 = SILVER 3 = GRAY
- 4 = BEIGE 5 = GREEN 6 = BLACK
- 7 = BROWN 8 = WHITE 9 = REDWOOD

510ft Slats Installed

\$ 2,968.00

Please Call Me If You
Have Any Questions

Thank
Dee



CONSTRUCTION COMPANY, INC

November 29, 1994

Mr. Stradford Coins
U.S. Army Corps of Engineers
New Orleans District
P.O. Box 60167
New Orleans, LA 70160-0267

RE: CONTRACT NO. DACW29-94-C-0079
LAKE PONTCHARTRAIN & VICINITY
HIGH LEVEL PLAN, LONDON AVENUE
OUTFALL CANAL, PARALLEL PROTECTION
MIRABEAU AVE TO LEON C. SIMON BLVD
FLOODWALL - ORLEANS PARISH, LA
B & K JOB NO. 9402
REQUEST FOR CHANGE NO. 002

Gentlemen:

We have enclosed our price of \$3,634.09 to install privacy slats in the existing chain link fence at our field office at 6201 Pratt Drive. We have quoted a fence which allows for 71% coverage. There are other types of slats which provide more coverage however the wind loading of these other types of fences are too great for the type of fence installed and could create some problems.

If you would like for us to quote some other type of fence please let us know and should you have any questions please do not hesitate to contact this office.

Sincerely,
B & K CONSTRUCTION CO., INC.


H. B. Kenyon,
President

HBK/kl
Enclosures

cc: Mr. Chester Ashley, Contracting Officer
Mr. Mike Tassin

9402/RFC2

CONTRACT DACW29-94-C-0079
 LAKE PONTCHARTRAIN AND VICINITY
 HIGH LEVEL PLAN, LONDON AVENUE
 OUTFALL CANAL, PARALLEL PROTECTION
 LEON C. SIMON BLVD. FLOODWALL
 ORLEANS PARISH, LOUISIANA
 B & K JOB NO. 9402, RFC NO. 002
 November 29, 1994

DESCRIPTION: COE requested price to panel weave privacy slats to existing chain link fence.

		Rate	Unit	Total
SUBCONTRACTS:				
ACE FENCE	Plastic privacy slats installed	2,968.00	1.00	2,968.00
OVERHEAD/PROFIT	G & A		13.90%	412.55
	SUBTOTAL			3,380.55
	PROFIT		7.50%	253.54
TOTAL COST				3,634.09

9402\RFC002.S5



CONSTRUCTION COMPANY, INC.

F A X C O V E R M E M O

TO: NAME: STRADFORD GOINS

 COMPANY: U.S.A.C.O.E.

 PHONE: _____ FAX: (504) 862-1226

FROM: NAME: Deborah Smith

 DATE: 11/30/94

REFERENCE: LONDON AVENUE CANAL

REQUEST FOR CHANGE NO. 2 (PROPOSAL)

PRIVACY SLATS FOR EXISTING CHAIN LINK FENCE

NUMBER OF PAGES INCLUDING THIS SHEET: 4

ORIGINAL TO FOLLOW BY MAIL:

YES NO UPON REQUEST

B&K
624 - 1866

288 5801 B&K Mike
288 - 8672 COE

ROUTING SLIP - ACTION/SUSPENSE COPY
 - SUSPENSE DATE:

CELMN-CD-NO	INITIAL	DATE
ASHLEY	AS	
BERNARD		
HABBAZ		
TUCKER		
SMITH		
ADAMS		

CELMN-CD-NO-E - OFFICE ENGINEER

MORTON		
PEREZ		
GOINS		
URBAN		
BRUNO		
HAGAN		
BLACKSTOCK		

CELMN-CD-NO-Q - LWR MISS RIVER & NO - VEN HP

FOGARTY		
BOURGEOIS		
DAVIS, D.		
CARR		
BLANCHARD		

CELMN-CD-NO-Q - LAKE PONT & CHAL AREA HP

DUHON		
BOUDREAUX		
WAGNER		
DAVIS, A.		
GONZALES		

CELMN-CD-NO-Q - BY BONFOUCA RES OFC

MORGAN		
MONTEGUT		
BRAKEL		
SHERMAN		
SMALLWOOD		

CELMN-CD-NO-Q - SWP & VICINITY

HINKAMP		
BURGESS, C.		
DERBES		
HARTLEY		
HUTSON		
SCARABIN		

CELMN-CD-NO-Q - UPR MISS RIVER & W JEFF HP

TILLY		
CRUMHOLT		
LAUTO		

CONST DIV, CONST MGMT SEC
 (FOR THE CONTRACT FILE)

NOAO FILE

REMARKS:

The Board of Commissioners

OF THE

Orleans Levee District

SUITE 202 — ADMINISTRATION BUILDING
NEW ORLEANS LAKEFRONT AIRPORT

New Orleans, La.

70126

TEL: 504-243-4000

PROTECTING YOU
AND YOUR FAMILY



November 9, 1994

Mr. Chester Ashley
CELMN-CD-NO
U. S. Army Corps of Engineers
P O Box 60267
New Orleans LA 70160-0267

RE: OLB Project No. 24908
London Avenue Canal - Phase III

Dear Mr. Ashley:


We have had several requests from residents on Pratt Drive that the contractor's staging area be made less objectionable to look at. Particularly offensive are the port-o-lets.

Possible solutions would be to relocate the port-o-lets, put slats in the chain link fence making them less visible or a combination of both.

In addition, there have been complaints about the contractor using Carlson Drive. Since it does not appear that its use is absolutely necessary by the contractor, he should not use it.

Please review these problems and advise what can be done to correct them. If there are any additional costs to be incurred it is understood they would be for OLD's account.

Sincerely,



Stevan G. Spencer, P. E.
Chief Engineer

SGS:pns

xc: Robert G. Harvey
Richard D. Sackett
Ted Lange
Beth Daniels
