

Barrier Berm Project – Daily Report

Day 142

Document: 139551-PMD-142-S

 \bigcirc

 \bigcirc

 \bigcirc

 \bigcirc

Date Prepared: October 21, 2010

Prepared by: Shaw Environmental & Infrastructure Group



E4 Berm – October 19, 2010



Barrier Berm Project 139551 – Daily Information

Yesterday – 20 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads		
East				
Cutter Alaska	41,640			
Subtotal East	41,640			
West				
Cutter California	42,867	12 Scows		
Cutter EW Ellefsen	22,474			
Cutter Texas	17,500			
Hopper Glenn Edwards	0	0		
Subtotal West	82,841	0		
Total	124,481	0		

Glenn Edwards still down for repairs, and is expected to return October 25th.

Today – 21 October


- Borrow operations at Pass a Loutre and West to continue.
- Berm placement operations to continue on E4 North, W10, and W8.

Tomorrow – 22 October

Today's operational activities to continue through tomorrow.

Potential Schedule Variability Items

· Final permit requirements, third party agency requirements.

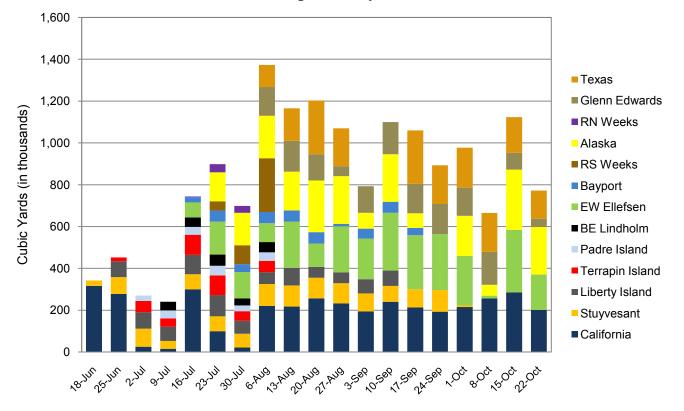

All Dredges Weekly Volume

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,782,074	
Cutter EW Ellefsen	2,716,126	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,291,886	
Cutter Texas	1,822,630	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,432,852	144
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	15,840,891	933

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,025,673
W8	468,167
W9	2,281,314
W10	1,123,119
W11	0
Borrow Operations	7,942,618
Totals	15,840,891

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	23,347
W8	1,250
W9	12,449
W10	7,630
W11	0
Totals	44,676

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – October 19, 2010



W8 & W9 Berm Operations - October 19, 2010
