



Barrier Berm Project – Daily Report

Day 148

Document: 139551-PMD-148-S

Date Prepared: October 27, 2010

Prepared by:

Shaw Environmental & Infrastructure Group



W10 & W9 Berms – October 26, 2010

Barrier Berm Project 139551 – Daily Information

Yesterday – 26 October

Vessel	Cubic Yards (CY) Handled	Hopper Loads
East		
Cutter Alaska	28,564	
Subtotal East	28,564	
West		
Cutter California	23,172	6 Scows
Cutter EW Ellefsen	6,582	
Cutter Texas	5,300	
Hopper Glenn Edwards	9,945	1
Subtotal West	44,999	1
Total	73,563	1

- Glenn Edwards returned to operations at 14:15 and performed 1 load.
- Lowered dredge production due to poor weather and rough seas.

Today – 27 October

- Borrow operations at South Pass to continue.
- Berm placement operations to continue on E4 North, W10, and W8.


Tomorrow – 28 October

- Today's operational activities to continue through tomorrow.

Potential Schedule Variability Items

- Final permit requirements, third party agency requirements.

All Dredges Weekly Volume

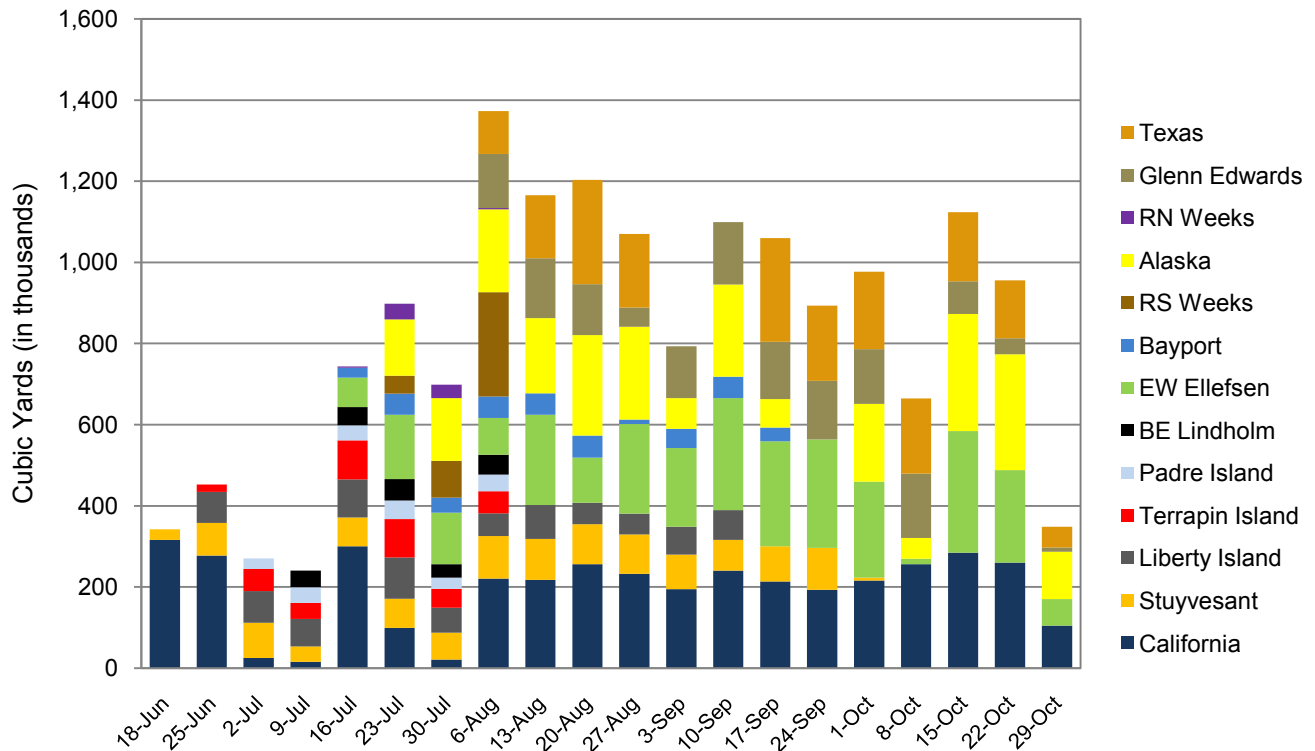

Barrier Berm Project 139551 – Cumulative Information

Inception to Date (ITD) Volume

Vessel	Handled - ITD (cy)	Hopper Loads - ITD
Cutter California	3,944,877	
Cutter EW Ellefsen	2,840,715	
Cutter RS Weeks *	391,350	
Cutter Alaska	2,467,454	
Cutter Texas	1,881,630	
Hopper Stuyvesant *	1,198,692	175
Hopper Liberty Island *	864,508	192
Hopper Bayport *	421,280	114
Hopper Glenn Edwards	1,442,797	145
Hopper Terrapin Island *	403,823	119
Hopper Padre Island *	216,133	84
Hopper BE Lindholm *	222,527	76
Hopper RN Weeks *	77,010	29
Total	16,372,796	934

* Demobilized from Project.

Progress by Berm and Borrow Operations (volume)

Location	Actuals (CY)
E3	0
E4	4,201,241
W8	592,756
W9	2,281,314
W10	1,182,119
W11	0
Borrow Operations	8,115,366
Totals	16,372,796

Progress by Berm (distance)

Location	Under Construction (LF)
E3	0
E4	24,747
W8	2,790
W9	12,449
W10	8,430
W11	0
Totals	48,416

Note: Under Construction represents linear footage of berm placed; all material may not yet conform to elevation +6.



E4 Berm – October 26, 2010



W10 Berm Operations – October 24, 2010
