BEB Production
Integrated Master Schedule
Current as of Wed 2/6/13

ID	Task Name	Duration	Start	Finish
1	**Release Final RFP**	0 days	Fri 1/25/13	Fri 1/25/13
2	**Proposals Due**	**0 days**	**Mon 3/11/13**	**Mon 3/11/13**
3	**SSEB**	**6 emons**	**Mon 3/11/13**	**Sat 9/7/13**
4	**Phase 2 Contract Award**	0 days	Sat 9/7/13	**Sat 9/7/13**
5	**Post-Award**	**599 days**	**Sat 9/7/13**	**Thu 12/24/15**
6	**Start of Work Meeting**	0 days	Mon 10/7/13	Mon 10/7/13
7	CDR	0 days	Wed 11/6/13	Wed 11/6/13
8	Pre-TRR	0 days	Mon 5/5/14	Mon 5/5/14
9	TRR	0 days	Thu 6/19/14	Thu 6/19/14
10	**LRIP**	**300 days**	**Mon 10/7/13**	**Mon 12/1/14**
11	Contractor Facility Preparation	240 edays	Mon 10/7/13	Wed 6/4/14
12	LRIP - Estimate 4/mo	6 emons	Wed 6/4/14	Mon 12/1/14
13	**PQT**	**363 days**	**Wed 6/4/14**	**Mon 10/26/15**
14	First Test Articles Delivered (4)	0 days	Wed 6/4/14	Wed 6/4/14
15	Second Test Articles Delivered (4)	0 days	Fri 7/4/14	Fri 7/4/14
16	All Test Articles Delivered (10)	0 days	Sun 8/3/14	Sun 8/3/14
17	I&KPT	30 edays	Wed 6/4/14	Fri 7/4/14
18	PQT	9 emons	Thu 6/19/14	Mon 3/16/15
19	Test Report	0 days	Mon 8/31/15	Mon 8/31/15
20	Safety Confirmation (POC is Steven Christy, AEC)	0 days	Mon 8/31/15	Mon 8/31/15
21	ATEC OMAR	0 days	Mon 10/26/15	Mon 10/26/15
22	**Logistics Tasks**	**599 days**	**Sat 9/7/13**	**Thu 12/24/15**
23	Provisioning	10 emons	Sat 9/7/13	Fri 7/4/14
24	FMECA	0 days	Fri 12/6/13	Fri 12/6/13
25	LORA	0 days	Sat 9/7/13	Sat 9/7/13
26	TMs/NMWR	8 emons	Sat 9/7/13	Mon 5/5/14
27	OER (Operational Evaluation Report - AEC)	0 days	Thu 12/24/15	Thu 12/24/15
28	**Logistics Demonstration**	**460 days**	**Sun 1/19/14**	**Sun 10/25/15**
29	Complete Test Resource Plan	0 days	Sun 1/19/14	Sun 1/19/14
30	Complete detailed LD Plan	0 days	Wed 6/18/14	Wed 6/18/14
31	Critical Task List selection	30 edays	Wed 6/18/14	Fri 7/18/14
32	Safety Release	0 days	Wed 9/17/14	Wed 9/17/14
33	LD Asset Available (1)	0 days	Thu 10/2/14	Thu 10/2/14
34	Log Demo Readiness Review	0 days	Thu 10/16/14	Thu 10/16/14
35	TM Validation	1 emon	Thu 10/16/14	Sat 11/15/14
36	Conduct Log Demo	1 emon	Wed 1/14/15	Fri 2/13/15
37	TM Verification	1 emon	Fri 9/25/15	Sun 10/25/15
38	**LUT**	**245 days**	**Mon 8/18/14**	**Mon 7/27/15**

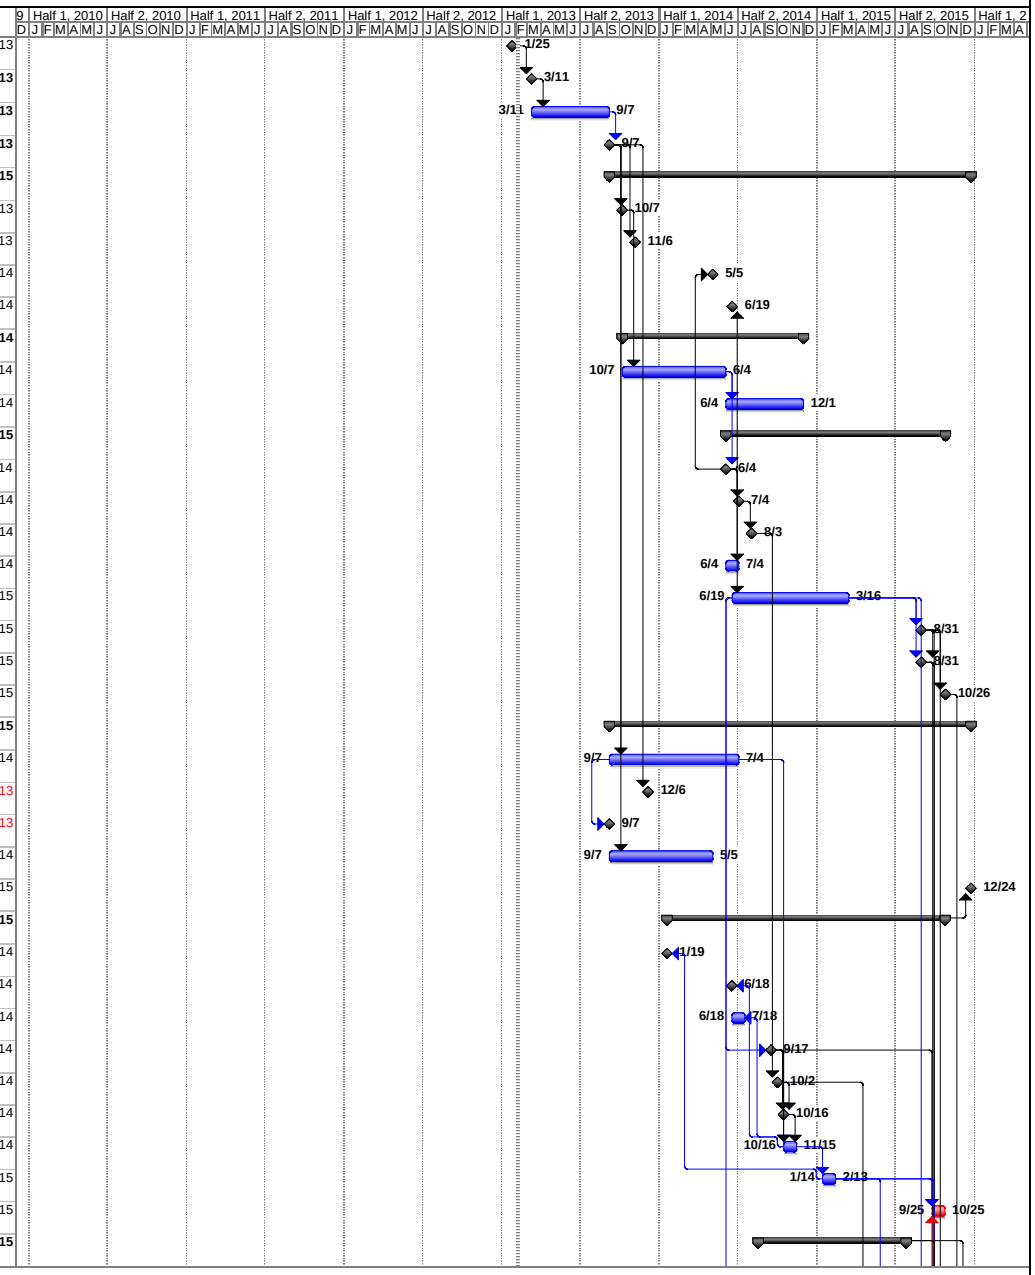

Project: Attachment 0005_BEB Produc
Date: Wed 2/6/13

Task	Milestone	Rolled Up Critical Task	Split	Group By Summary
Critical Task	Summary	Rolled Up Milestone	External Tasks	Deadline
Progress	Rolled Up Task	Rolled Up Progress	Project Summary	

BEB Production
Integrated Master Schedule
Current as of Wed 2/6/13

ID	Task Name	Duration	Start	Finish
39	Safety Release	0 days	Mon 8/18/14	Mon 8/18/14
40	All LUT Assets Delivered	0 days	Thu 4/30/15	Thu 4/30/15
41	LUT (Fast Water)	60 edays	Thu 5/28/15	Mon 7/27/15
42	Physical Configuration Audit	14 edays	Mon 8/31/15	Mon 9/14/15
43	TC - FMR	0 days	Mon 10/12/15	Mon 10/12/15
44	**FRP Decision**	0 days	Mon 10/26/15	Mon 10/26/15



Project: Attachment 0005_BEB Produc
Date: Wed 2/6/13

Task
Critical Task
Progress
Milestone
Summary
Rolled Up Task
Rolled Up Critical Task
Rolled Up Milestone
Rolled Up Progress
Split
External Tasks
Project Summary
Group By Summary
Deadline
